


Project Name: I-70 Floyd Hill East Section
 Project Number: 25174
 Date: April 2024 Update

I-70 Floyd Hill East Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

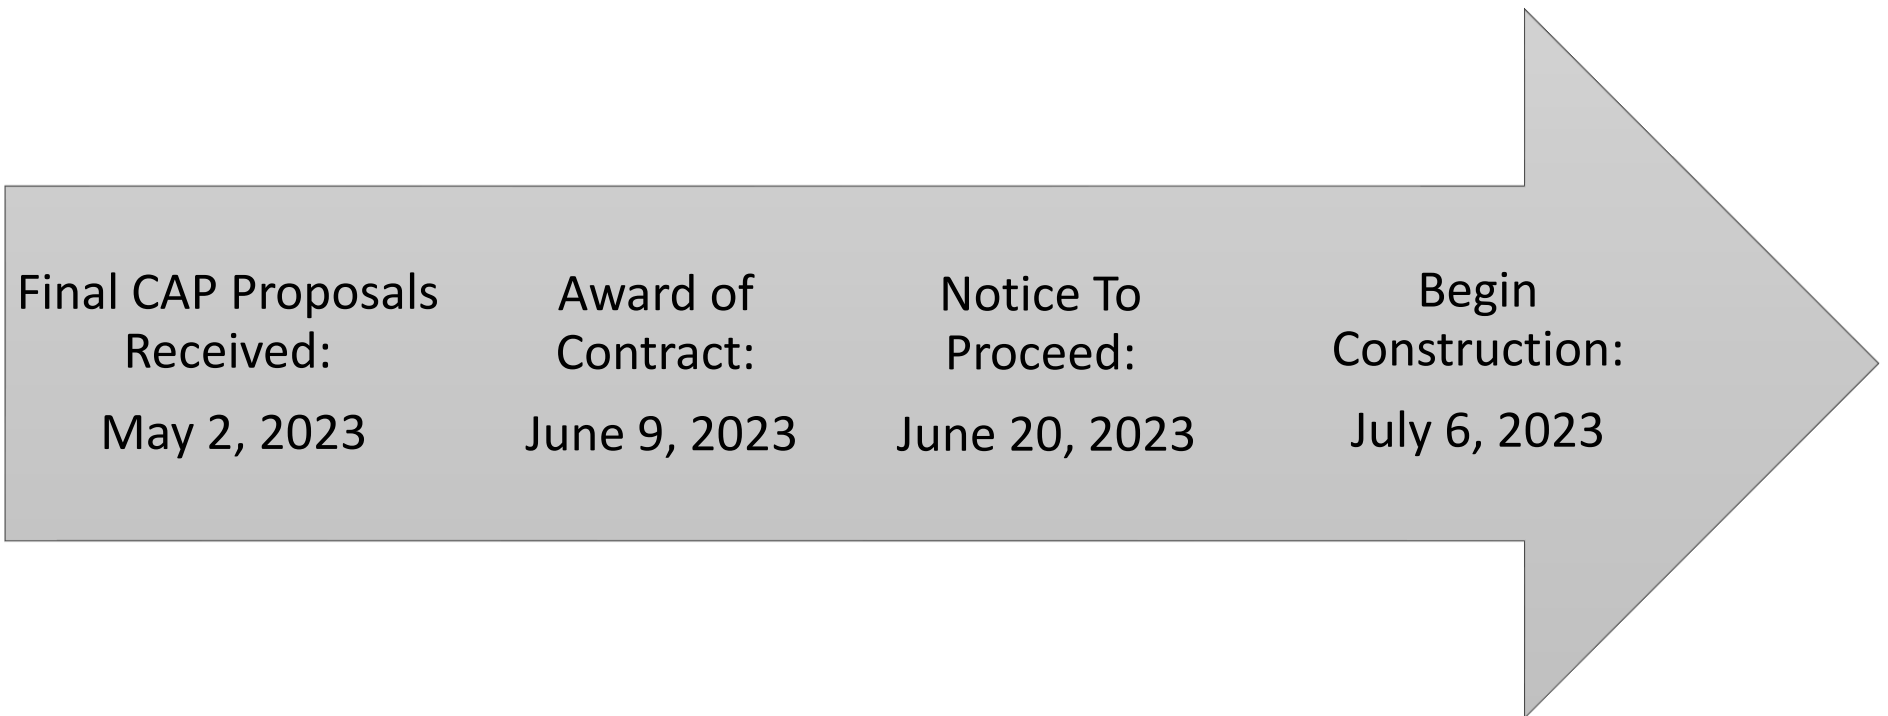

Final CAP Proposals Received: May 2, 2023

Award of Contract: June 9, 2023

Notice To Proceed: June 20, 2023

Begin Construction: July 6, 2023




Project Name: I-70 Floyd Hill East Section

Project Number: 25174

Date: April 2024 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

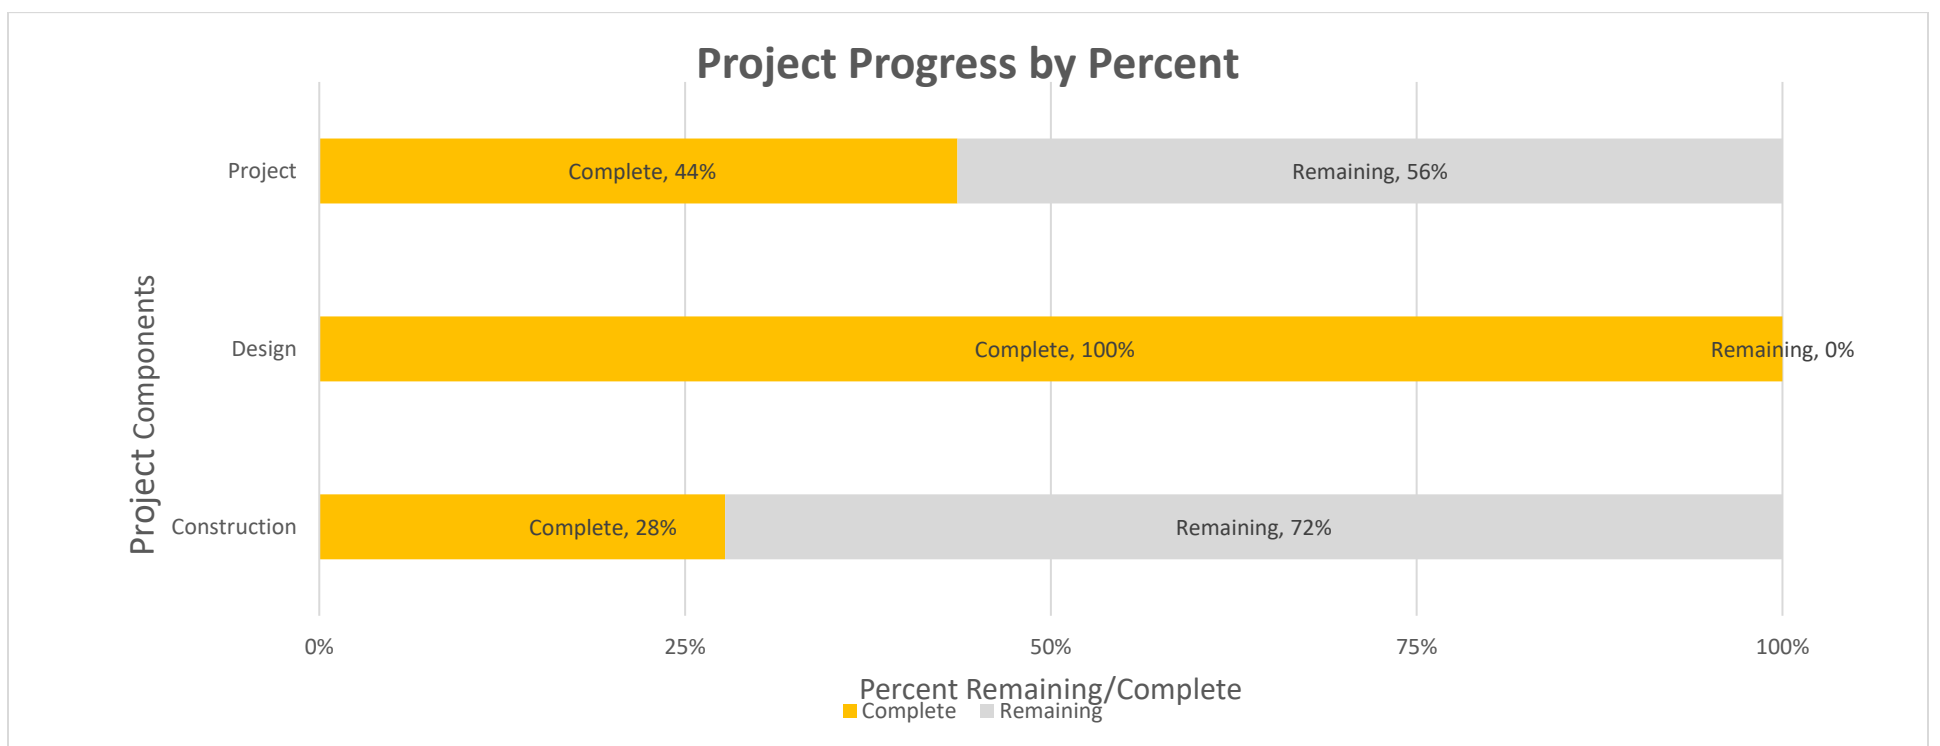

Overall Project: 44% Complete, 56% Remaining

Design: 100% Complete, 0% Remaining

Construction: 28% Complete, 72%

Remaining




Project Name: I-70 Floyd Hill East Section

Project Number: 25174

Date: April 2024 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

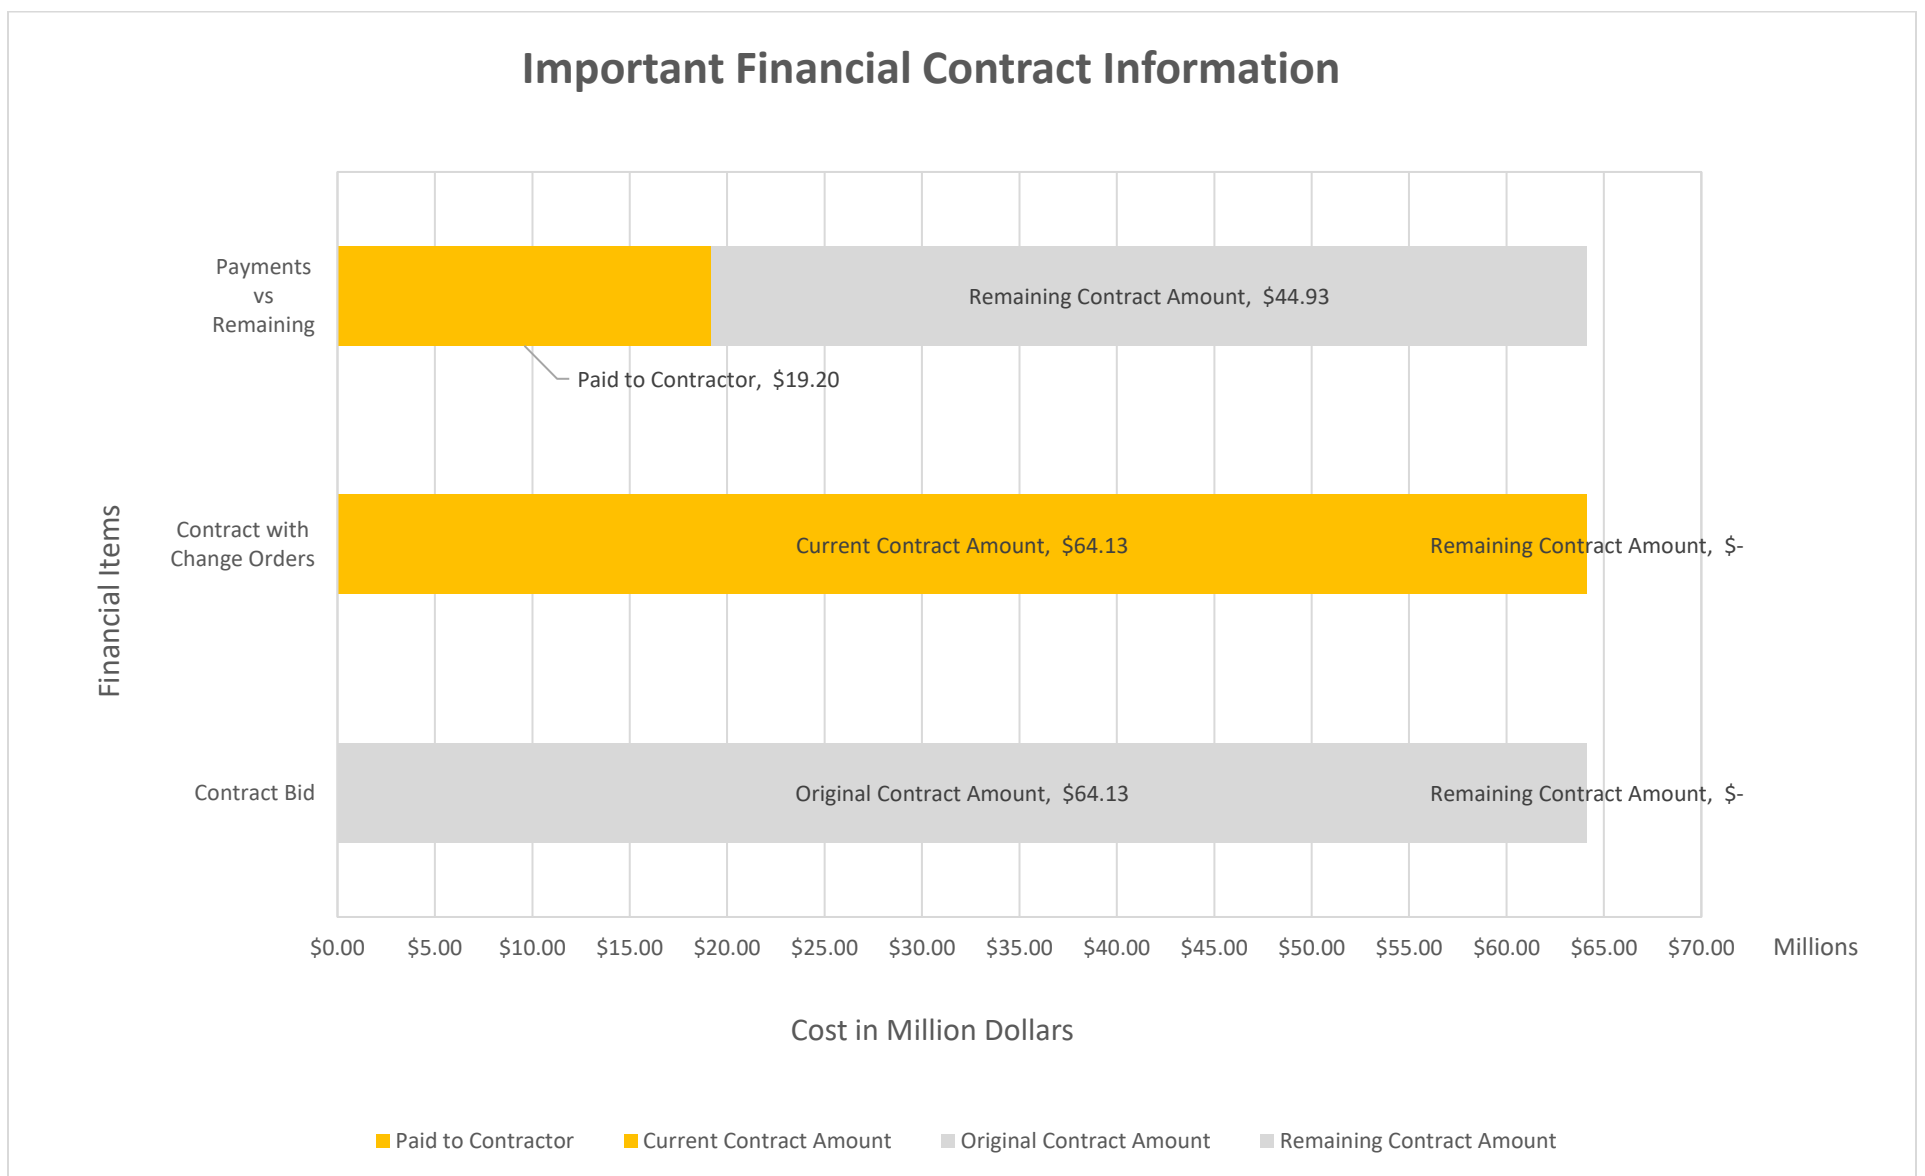

Initial Contract Value: \$64.13 Million

Payments to date: \$19.20 Million, Payments remaining \$44.93 Million

Current Contract Value: \$64.13 Million, Total Change Orders to Date: \$0




Project Name: I-70 Floyd Hill East Section

Project Number: 25174

Date: April 2024 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

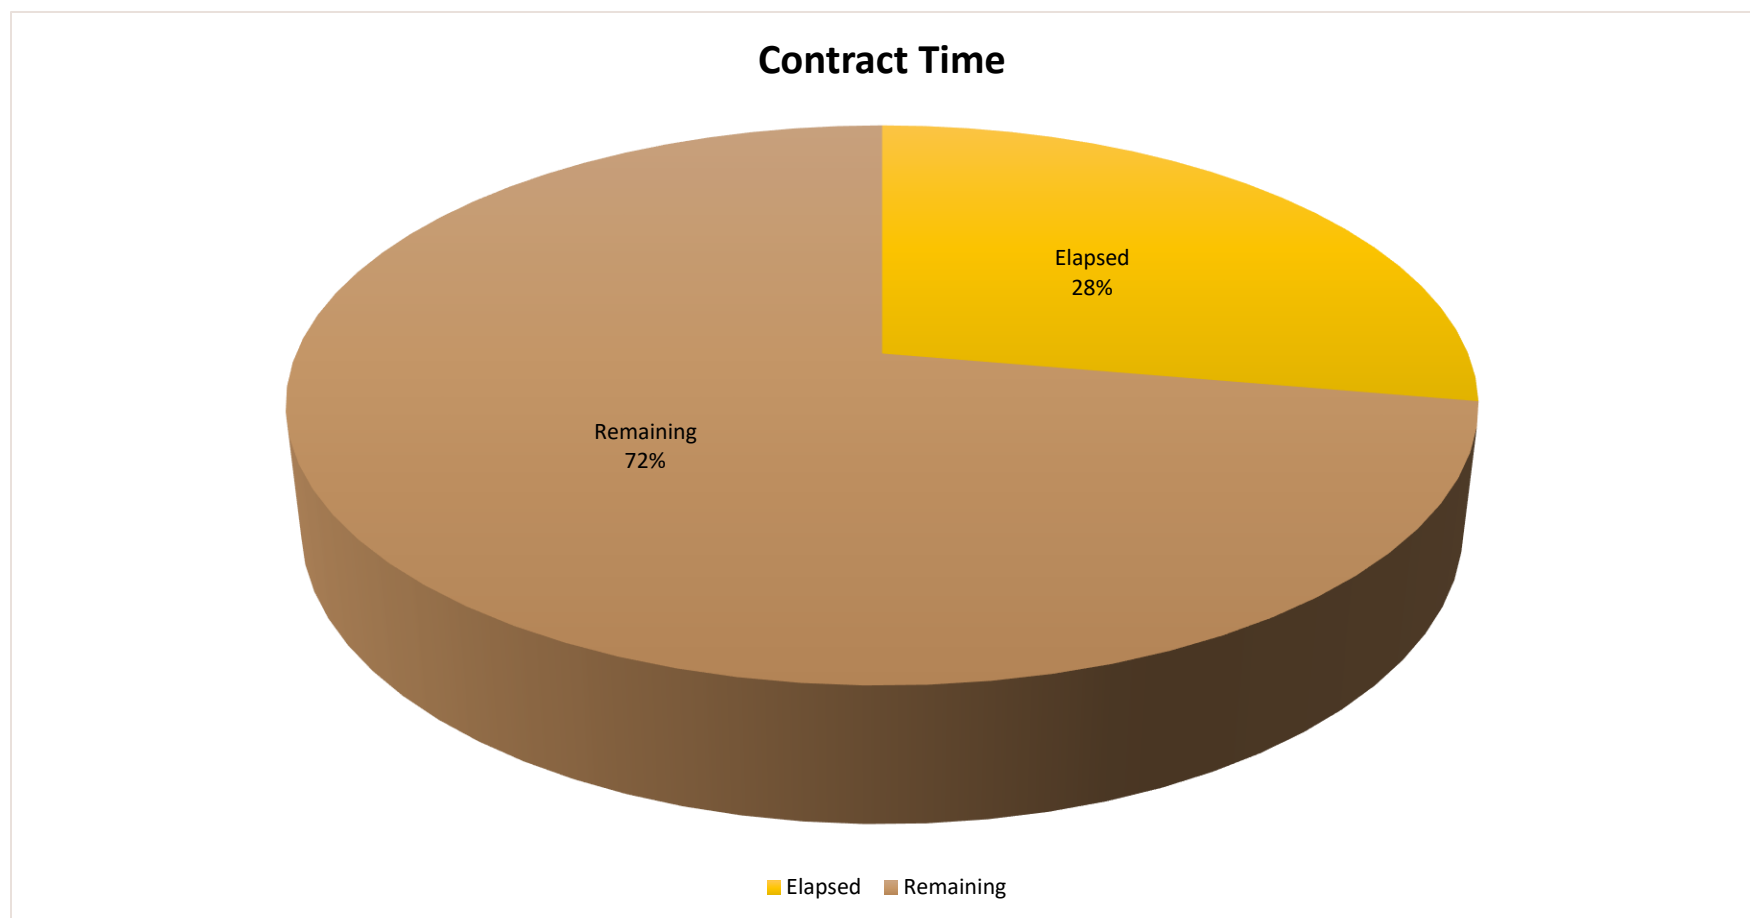

Total Contract time: 1136 Calendar Days

Elapsed Contact time: 315 days, 28%

Contract Time Remaining: 821 days, 72%
