




Project Name: I-70 Floyd Hill Central Section  
Project Number: 25177  
Date: April 2024 Update

## I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

### Key Dates

The following image shows the progression of the key project dates.

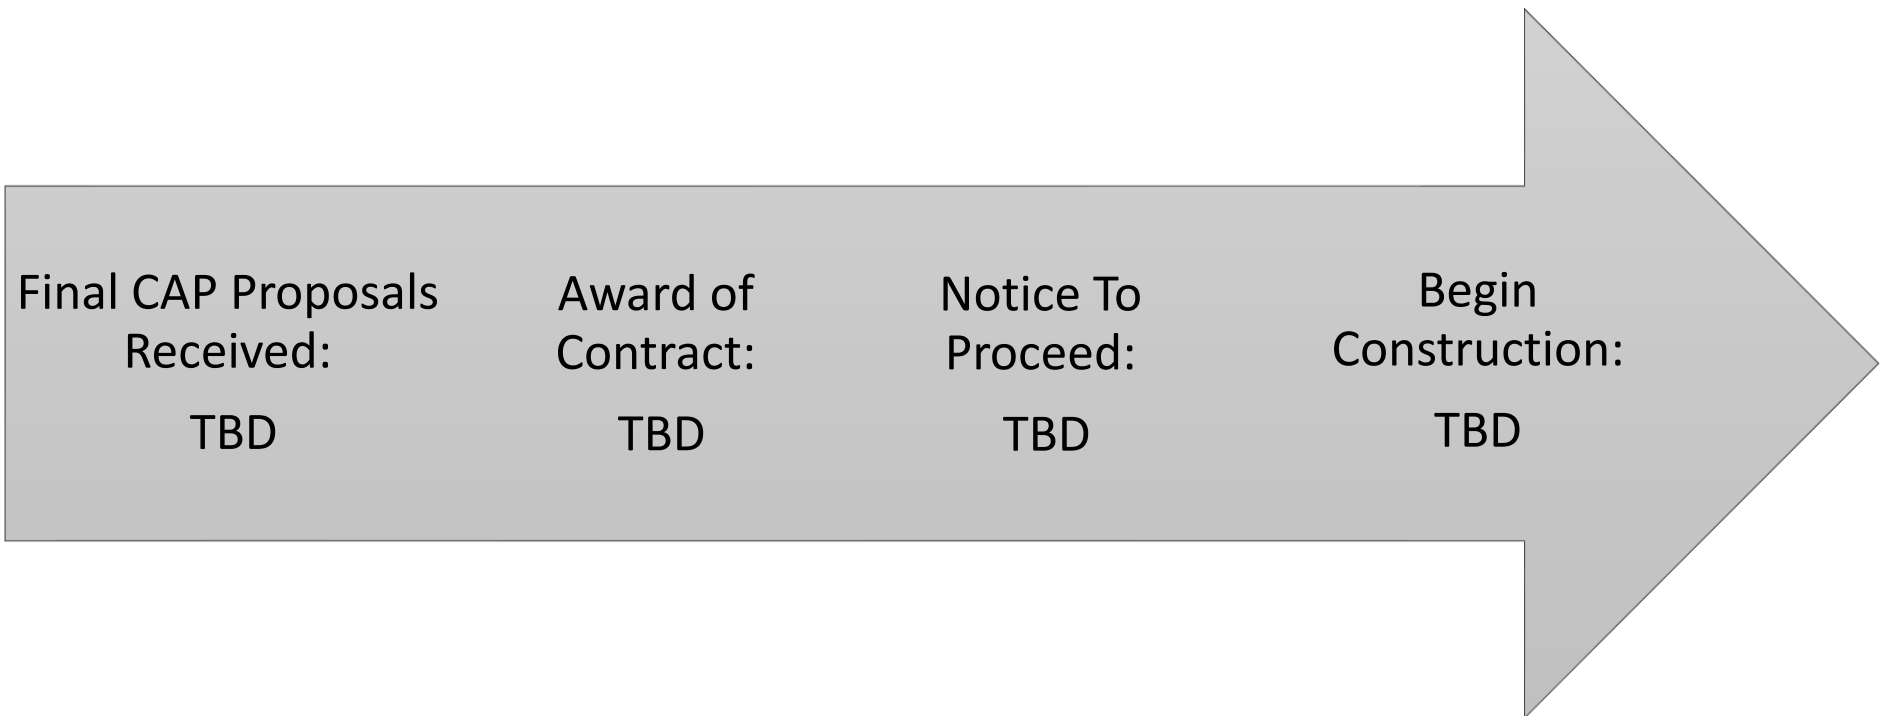

Final CAP Proposals Received: TBD

Award of Contract: TBD


Notice To Proceed: TBD

Begin Construction: TBD

Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: April 2024 Update

### Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

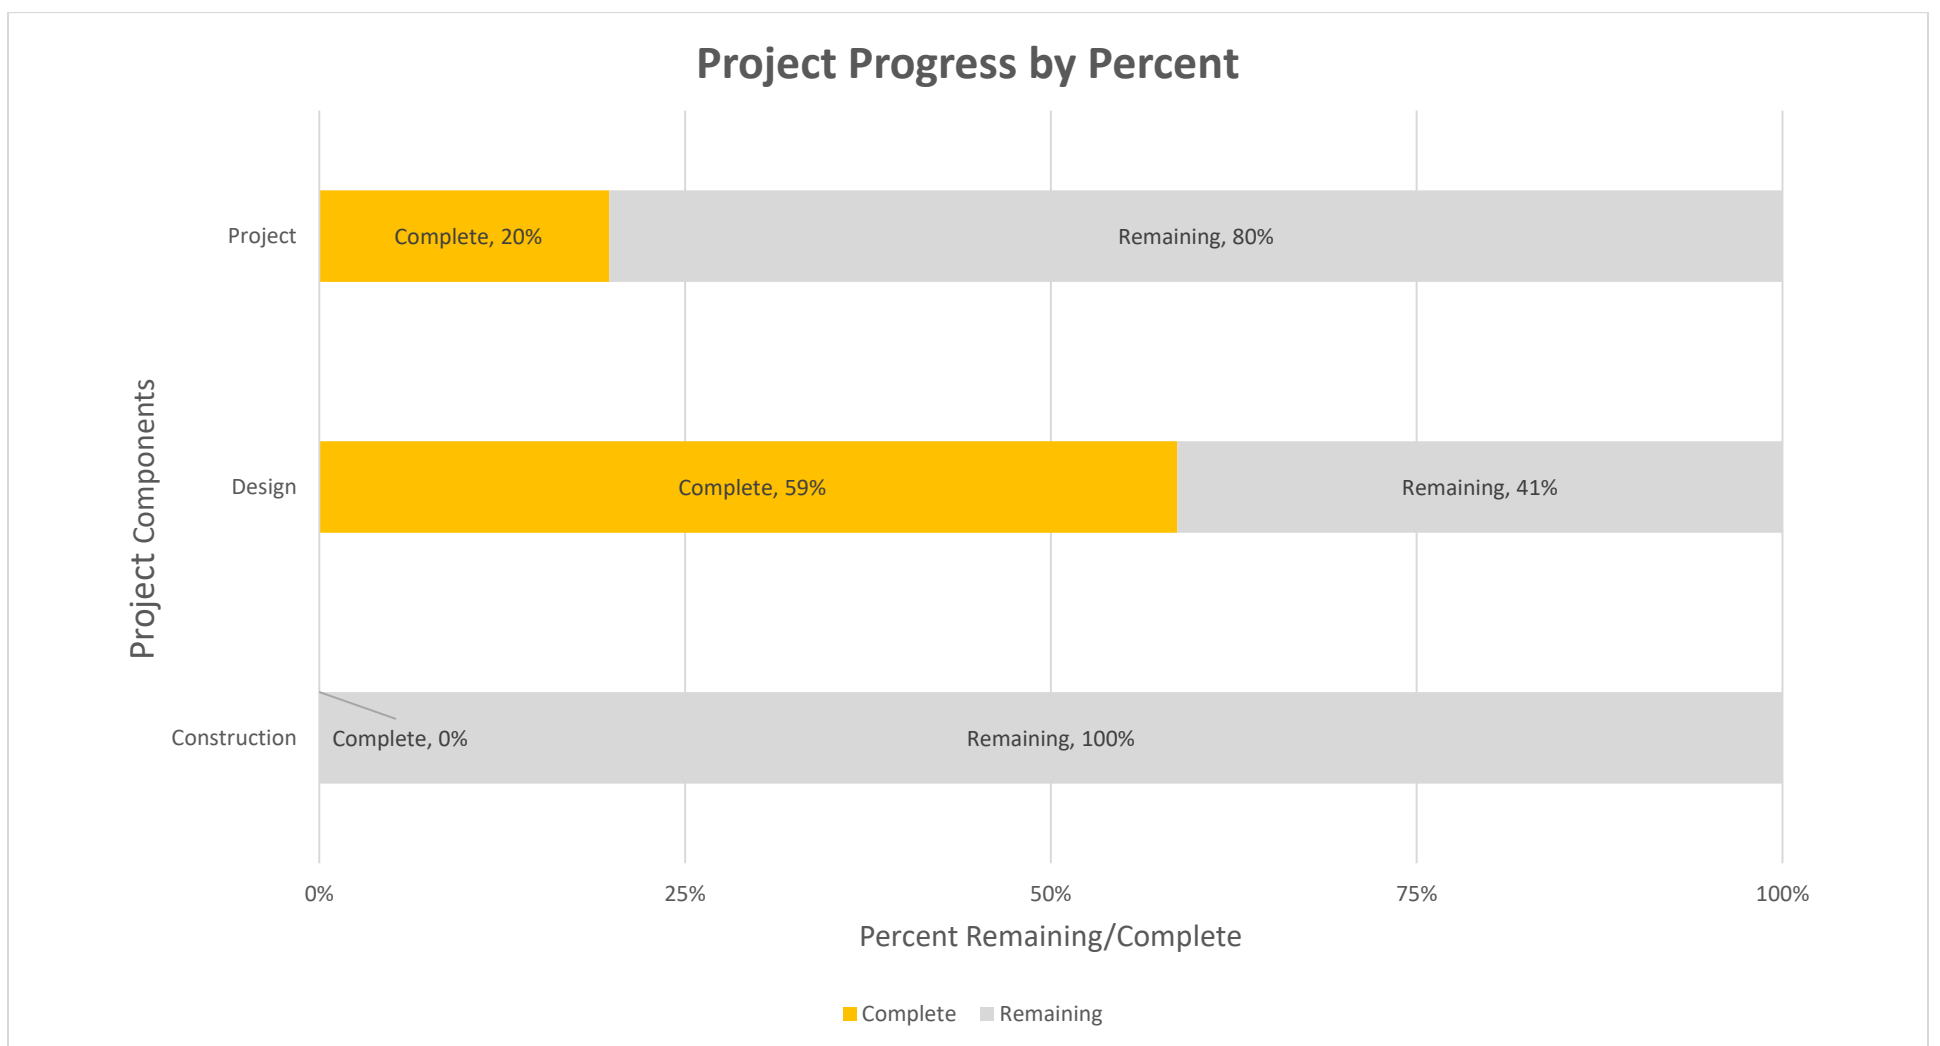

Overall Project: 20% Complete, 80% Remaining


Design: 59% Complete, 41% Remaining

Construction: 0% Complete, 100% Remaining

Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: April 2024 Update

### Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

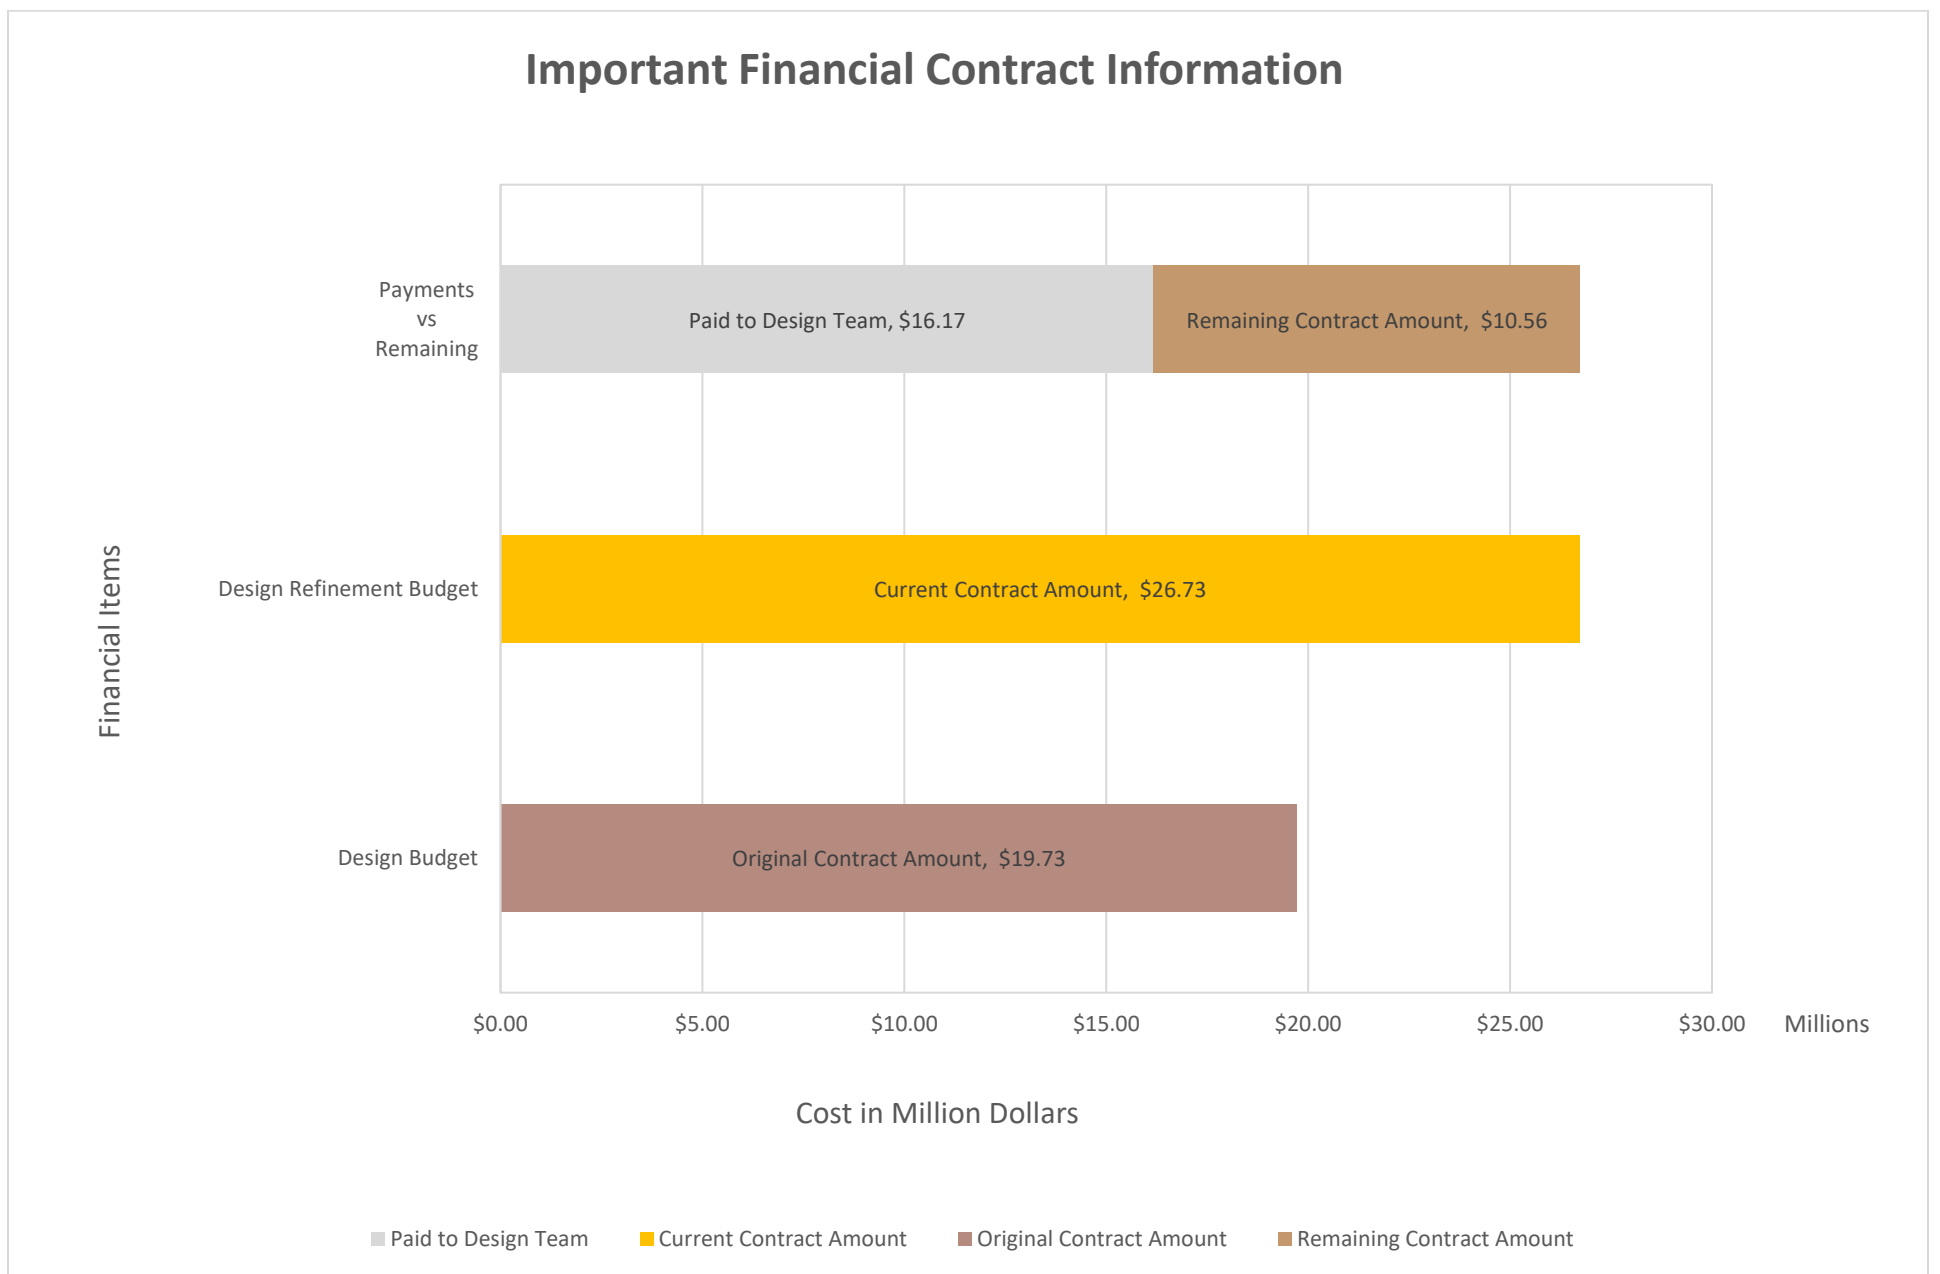

Initial Design Contract Value: \$19.73 Million

Design Payments to date: \$16.17 Million, Payments remaining \$10.56 Million

Current Design Contract Value: \$26.73 Million, Total Change Orders to Date: \$7 Million




Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: April 2024 Update

## Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

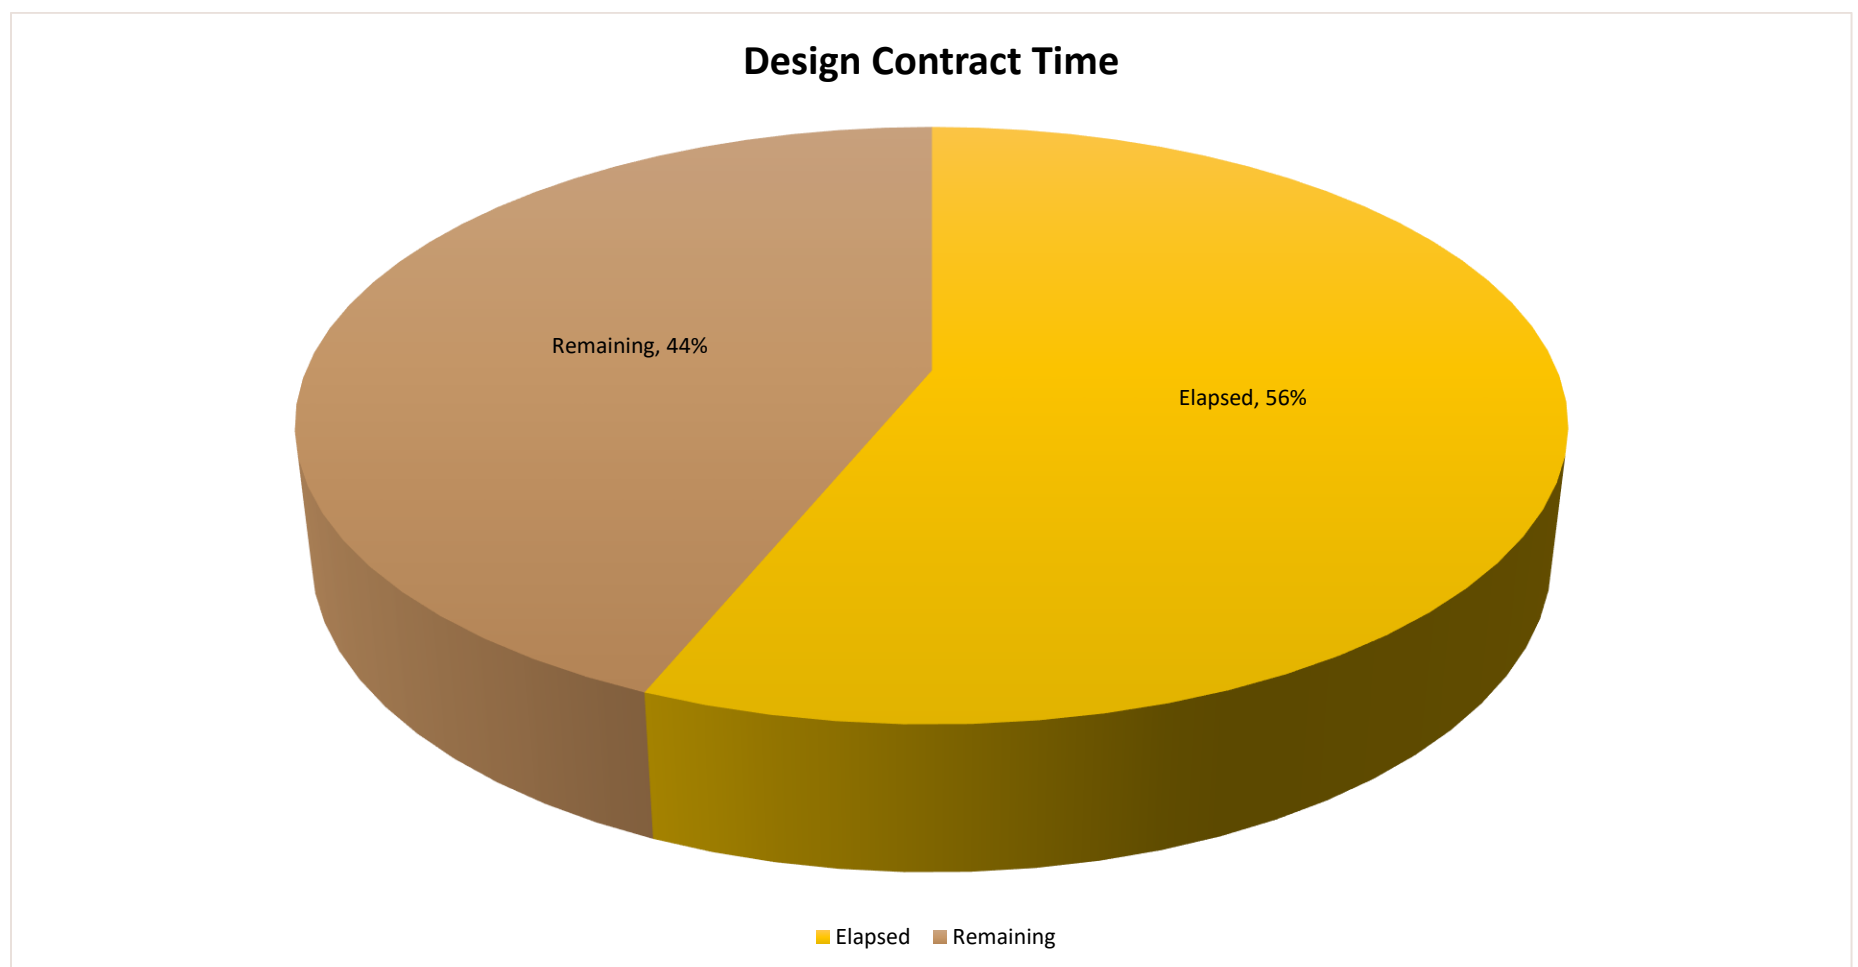

Total Design Contract time: 596 days

Elapsed Design Contract time: 335 days, 56%

Design Contract Time Remaining: 261 days, 44%
