



Project Name: Vasquez Blvd – I-270 to 64th Avenue

Project Number: 22922


Date: 11/4/2024 Update

Vasquez Blvd – I-270 to 64th Avenue Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

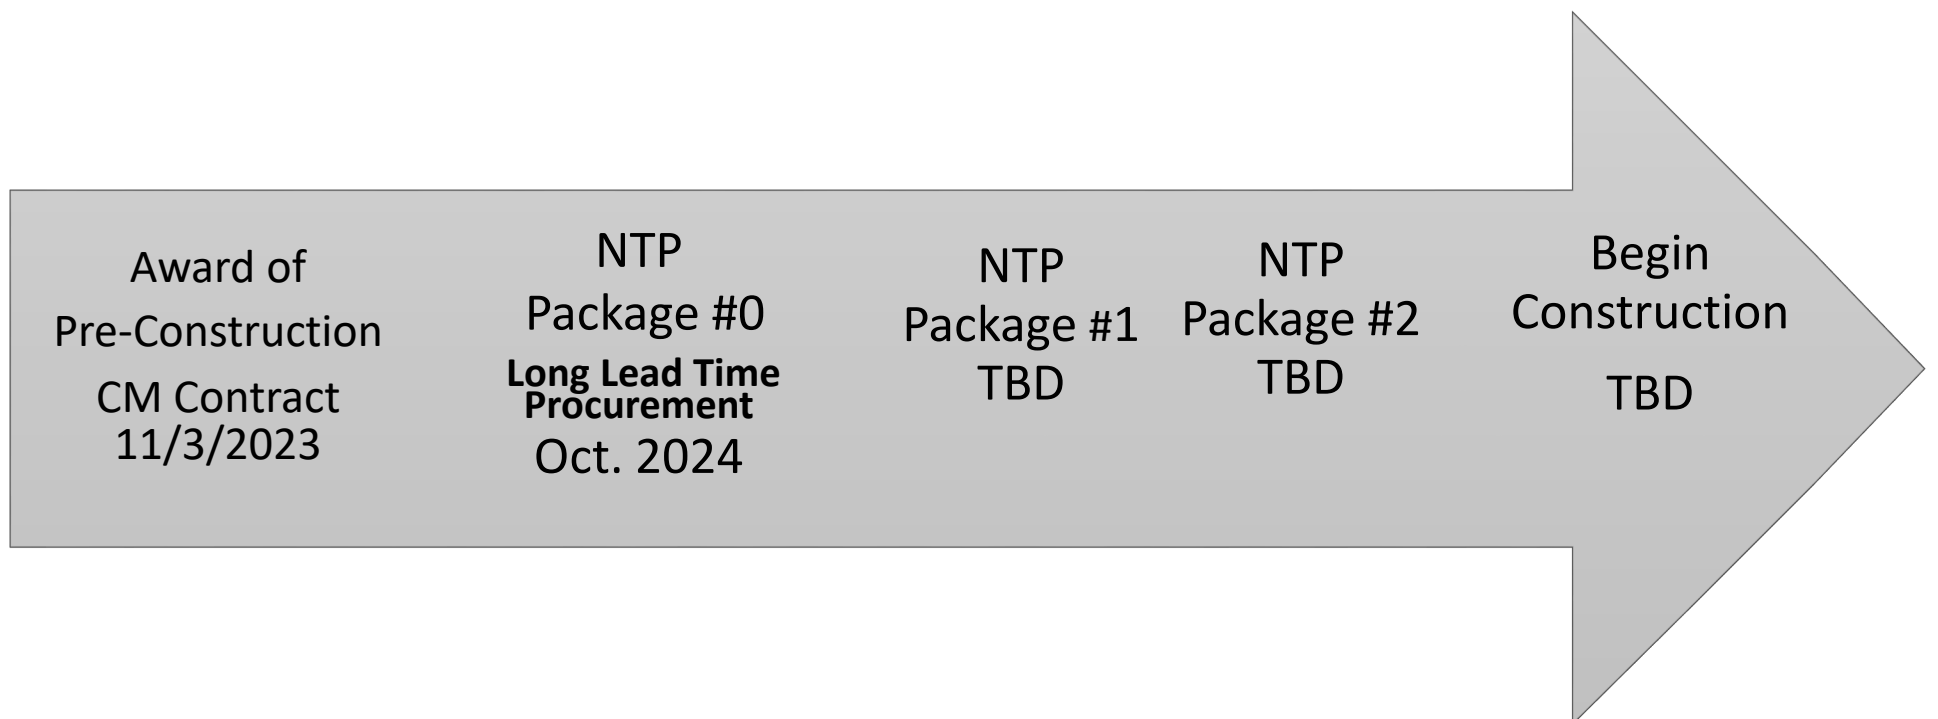

Award of Pre-Construction CM Contract: 11/3/2023

Notice to Proceed Package #0: October 2024

Notice to Proceed Package #1: TBD

Notice to Proceed Package #2: TBD

Begin Construction: TBD




Project Name: Vasquez Blvd – I-270 to 64th Avenue

Project Number: 22922

Date: 11/4/2024 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

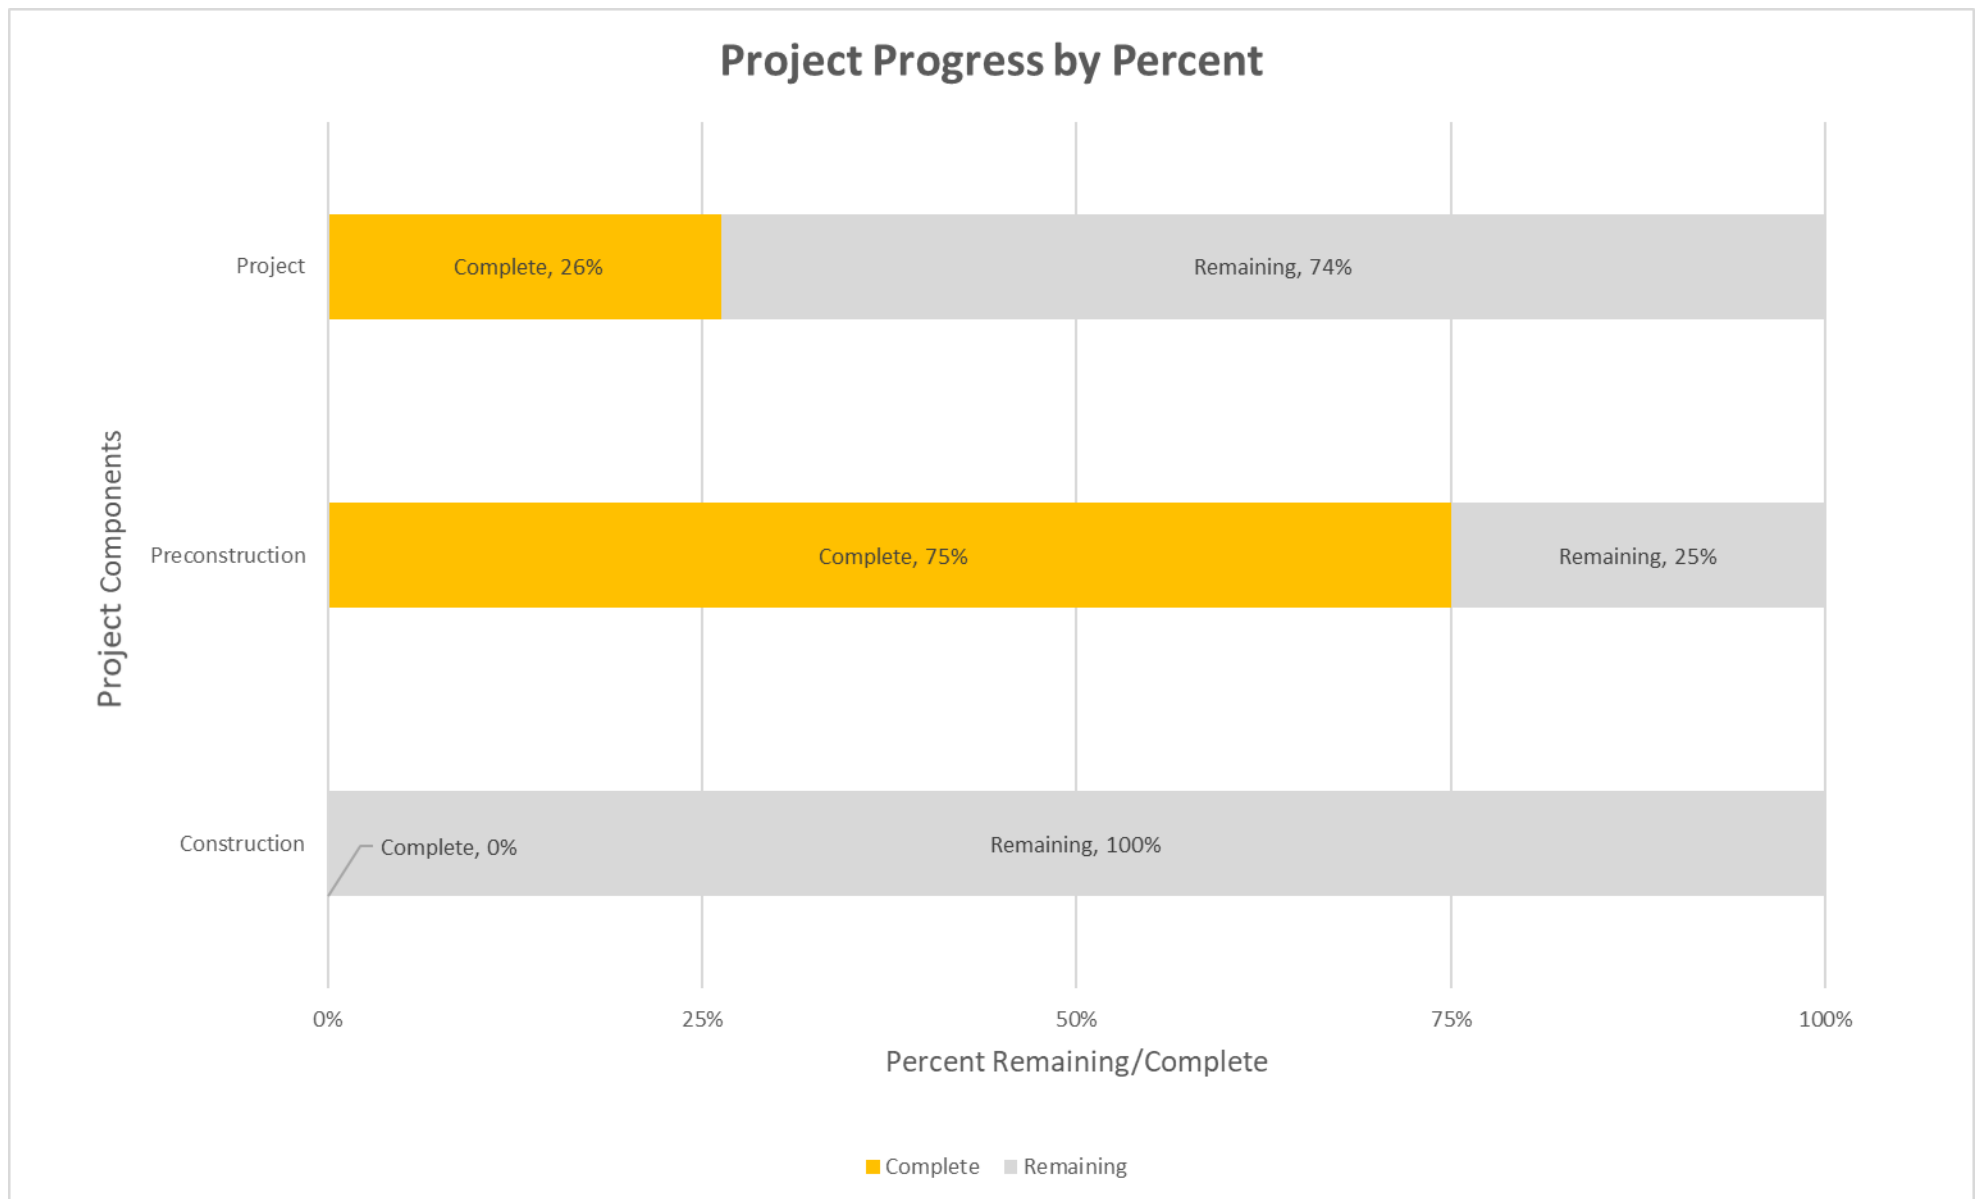

Overall Project: 26% Complete, 74% Remaining

Design: 75% Complete, 25% Remaining

Construction: 0% Complete, 100% Remaining

Project Name: Vasquez Blvd – I-270 to 64th Avenue

Project Number: 22922

Date: 11/4/2024 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.



Initial Contract Value: \$200,000

Payments to date: \$122,760 Payments remaining – \$77,240

Current Contract Value: TBD, Total Change Orders to Date: N/A

Initial Contract Value: TBD


Project Name: Vasquez Blvd – I-270 to 64th Avenue

Project Number: 22922

Date: 11/4/2024 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

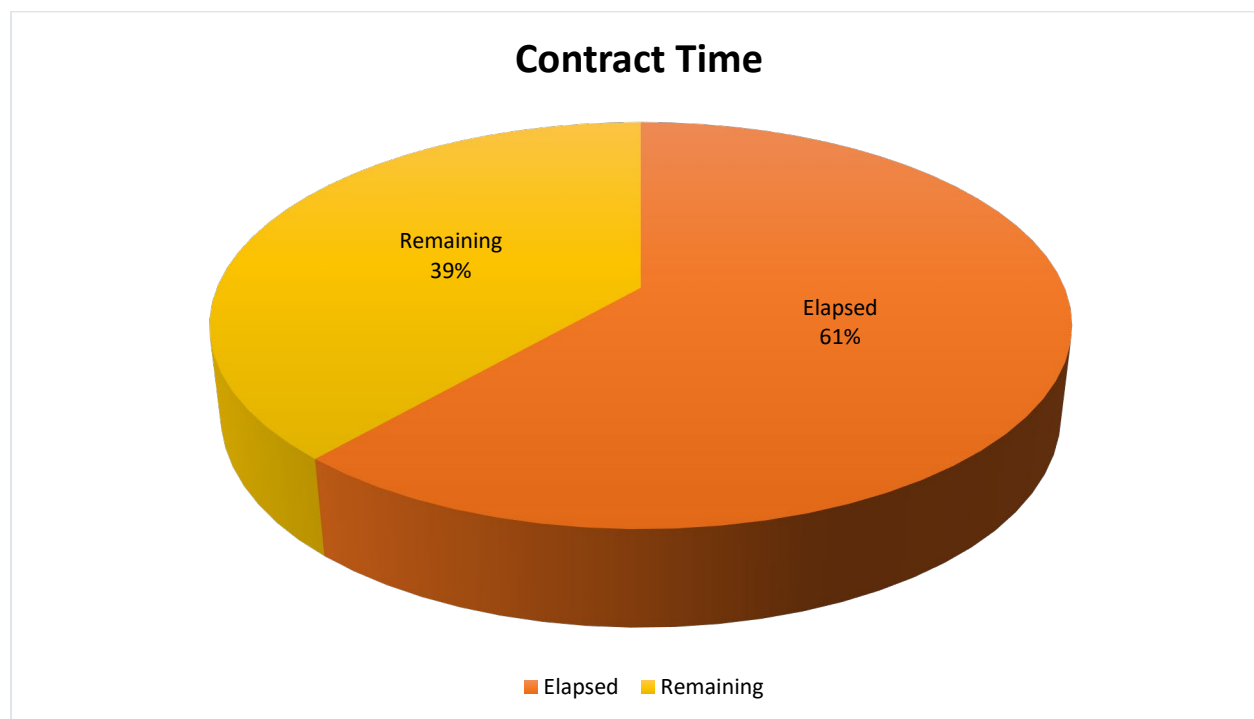

Total Contract time: 200 days

Elapsed Contact time: 123 days, 61%

Contract Time Remaining: 77, 39%
