


I-270 Critical Bridges Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.



1

Final CAP Proposal Received: To Be Determined

Award of Contract: To Be Determined


Notice to Proceed: To Be Determined

Begin Construction: To Be Determined



Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

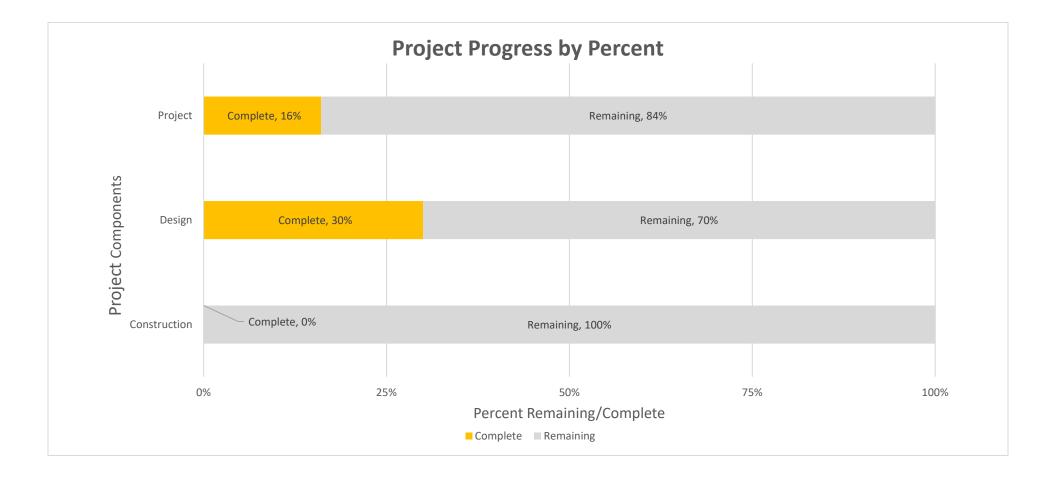

Overall Project: 16% Complete, 84% Remaining


Design: 30% Complete, 70% Remaining

Construction: 0% Complete, 100% Remaining



Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract's bid amount.

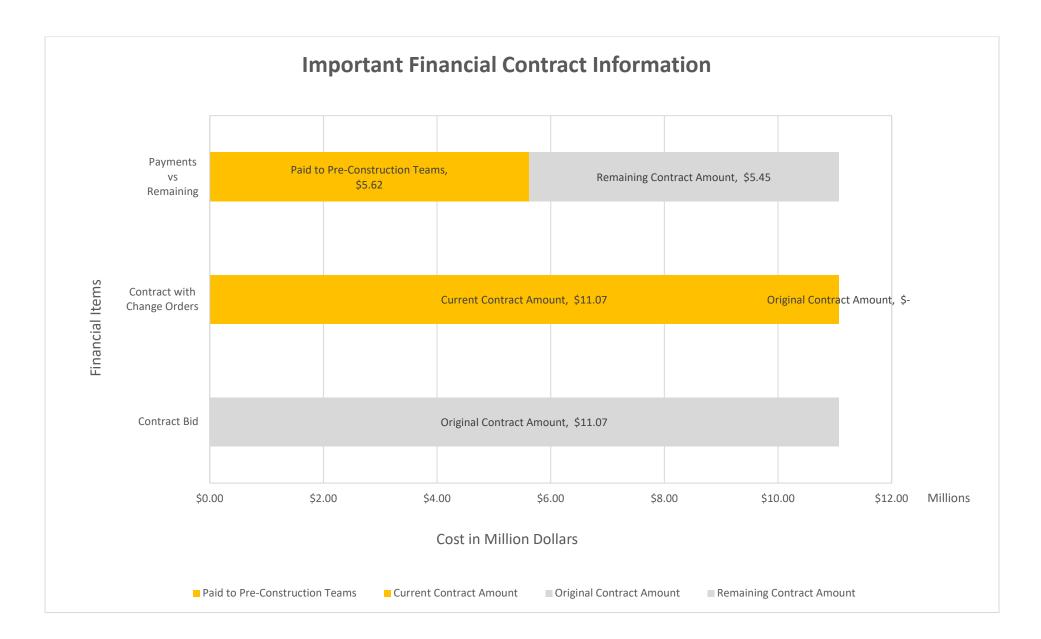

Initial Pre-Construction Contracts Value: \$11.07 Million

Payments to date: \$5.62 Million, Payments remaining \$5.45 Million


Current Contracts Value: \$11.07 Million, Total Change Orders to Date: \$0

Initial Contracts Value: \$11.07 Million



Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

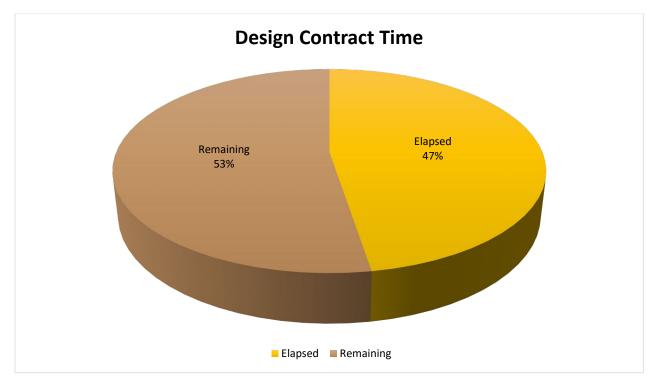

Total Contract time: 1314 Calendar Days

Elapsed Contact time: 623 days, 47%

Contract Time Remaining: 691 days, 53%
