


# I-270 Critical Bridges Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

#### **Key Dates**

The following image shows the progression of the key project dates.

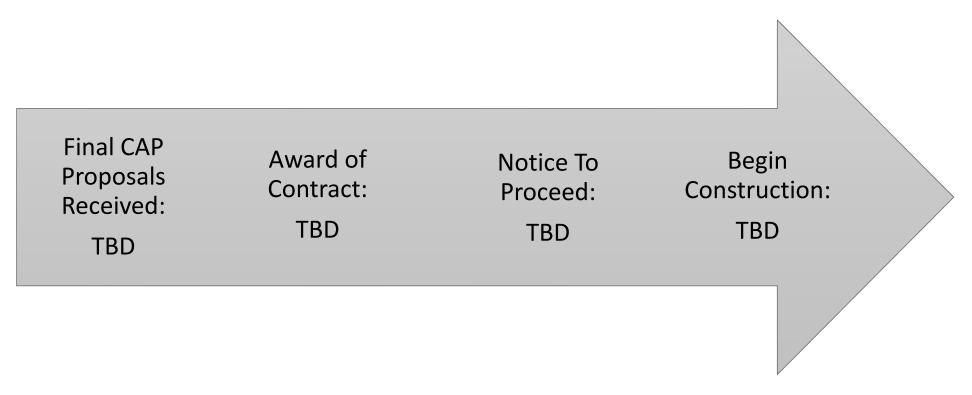

1

Final CAP Proposal Received: To Be Determined

Award of Contract: To Be Determined


Notice to Proceed: To Be Determined

Begin Construction: To Be Determined



### **Project Progress by Percent**

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

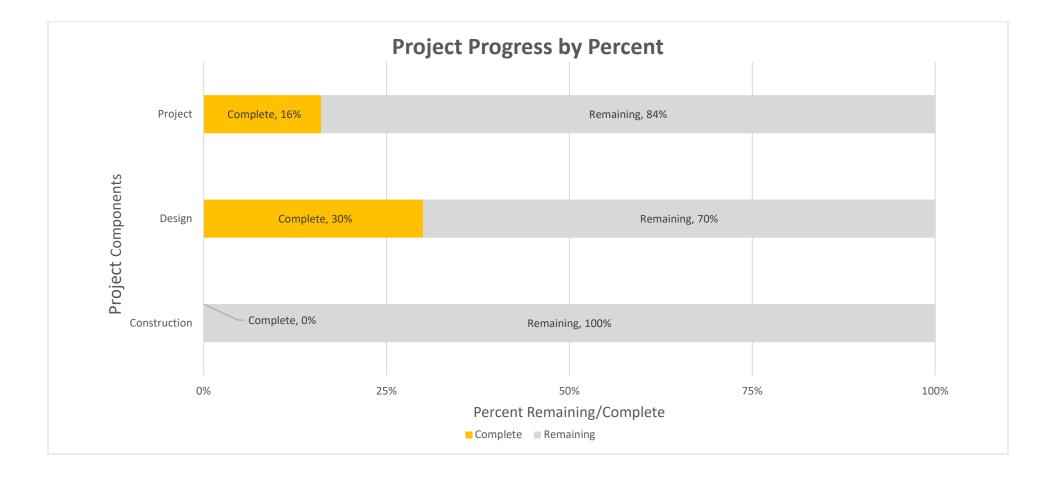

Overall Project: 16% Complete, 84% Remaining


Design: 30% Complete, 70% Remaining

Construction: 0% Complete, 100% Remaining



### **Important Financial Contract Information**

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract's bid amount.

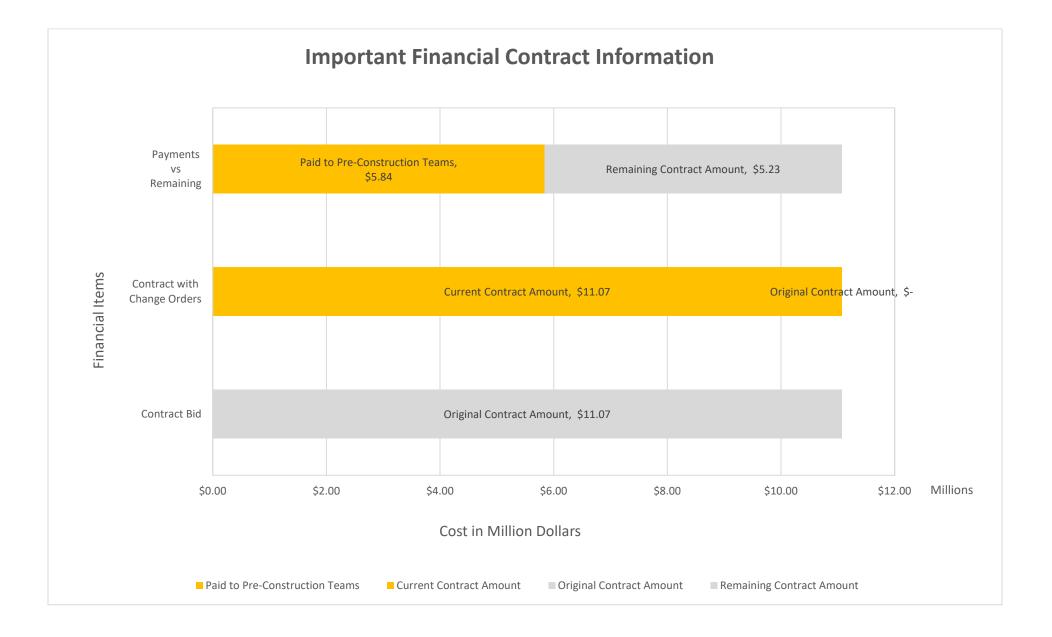

Initial Pre-Construction Contracts Value: \$11.07 Million

Payments to date: \$5.84 Million, Payments remaining \$5.23 Million


Current Contracts Value: \$11.07 Million, Total Change Orders to Date: \$0

Initial Contracts Value: \$11.07 Million



# **Contract Time**

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

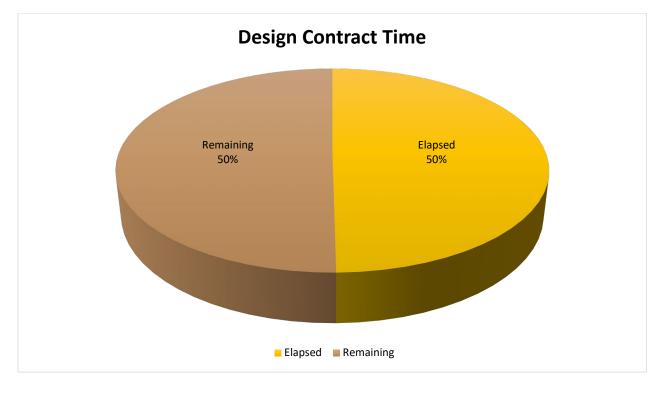

Total Contract time: 1314 Calendar Days

Elapsed Contact time: 654 days, 50%

Contract Time Remaining: 660 days, 50%
