


# I-270 Critical Bridges Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

#### **Key Dates**

The following image shows the progression of the key project dates.

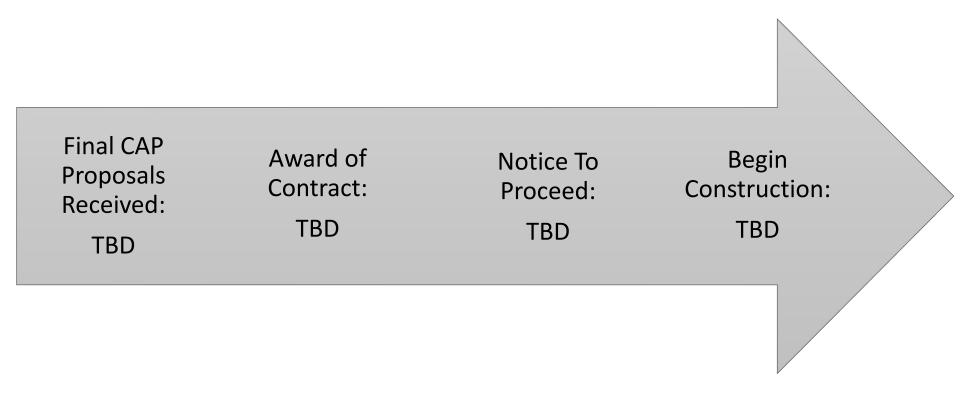

1

Final CAP Proposal Received: To Be Determined

Award of Contract: To Be Determined


Notice to Proceed: To Be Determined

Begin Construction: To Be Determined



## **Project Progress by Percent**

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

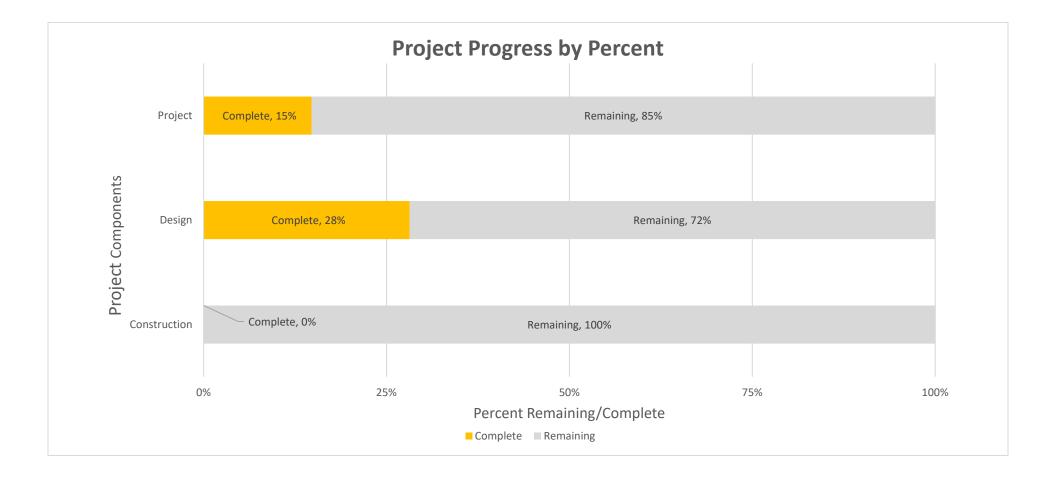

Overall Project: 15% Complete, 85% Remaining


Design: 28% Complete, 72% Remaining

Construction: 0% Complete, 100% Remaining



#### **Important Financial Contract Information**

The following Bar chart shows the projects payments vs remaining amount, total current contract vale and change orders to date, and contract's bid amount.

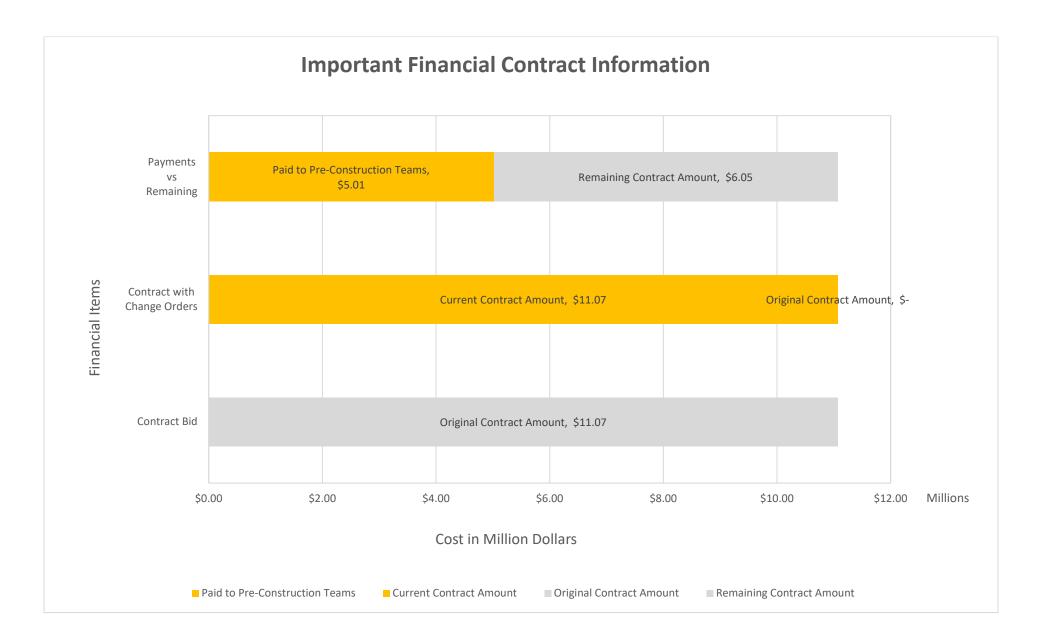

Initial Pre-Construction Contracts Value: \$11.07 Million

Payments to date: \$5.01 Million, Payments remaining \$6.05 Million


Current Contracts Value: \$11.07 Million, Total Change Orders to Date: \$0

Initial Contracts Value: \$11.07 Million



## **Contract Time**

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

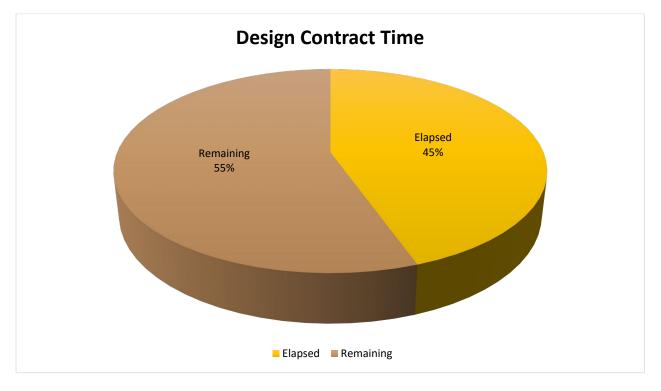

Total Contract time: 1262 Calendar Days

Elapsed Contact time: 562 days, 45%

Contract Time Remaining: 700 days, 55%
