

# September 2018

## Monthly Operations Report



## Table of Contents

1.0	Volumes and Lane Usage .....	3
2.0	Revenues .....	5
3.0	Operational Incidents, Issues, and Closures .....	5
4.0	Mean Time Between Failure (MTBF) and Mean Time to repair (MTTR) .....	7
5.0	Hybrid Utilization .....	7

### TABLES

Table 1 – Monthly Traffic Summaries .....	4
Table 2 – Managed Lanes Closures to Date .....	6
Table 3 – ETCS Issues per CA Schedule 6 Appendix 6-2 .....	6
Table 4 - Status of Noncompliance Categories .....	7
Table 5 – Mean Time Between Failure & Mean Time To Repair .....	7
Table 6 – Hybrid Utilization .....	7

### FIGURES

Figure 1 – Monthly Traffic Distribution .....	4
Figure 2 – Daily Traffic Counts .....	5

# INTRODUCTION

Pursuant to Schedule 6, Section 1.8.2(a) of the Concession Agreement, Plenary Roads Denver (“PRD”) is required to submit a monthly report covering all essential statistics related to the Managed Lanes. The following data covers the month of September 2018. Operationally, September was a positive month. Several routine maintenance tasks were completed, there were minimal incidents to maintained elements, and traffic volumes were consistent with expectations.

## 1.0 VOLUMES AND LANE USAGE

Over the last several months as more commuters use the transponders for either ExpressToll™ (AVI) or HOV travel, License Plate (LPT) transactions have consistently decreased as a percentage of total traffic volume. The total monthly gantry traffic volume for September 2018 in the I-25 Central and US 36 Managed Lanes was 293,035 and 1,491,083, respectively.

The table below provides the monthly summary for each Managed Lanes roadway, along with a detailed breakdown of weekday volumes. For reference, the AM Peak Period is considered to be weekdays from 6:45 am – 8:45 am. The PM Peak Period is considered to be, weekdays, from 4:15pm – 5:45pm. It should be noted, that the I-25 Managed Lane traffic reflects traffic counts from a single gantry and US 36 Managed Lane counts reflect fourteen gantries, seven gantries in each direction. Therefore, US 36 data will indicate far greater traffic counts that are not comparative to those of I-25.

The following charts depict the distribution of traffic by type (Figure 1) and the daily traffic counts (Figure 2) and for the month.

Traffic Summary (US 36)						
	AVI	LPT	HOV	Non-Rev & Hybrid	Total	Hybrid
<b>Total Monthly Traffic</b>	843,956	366,484	242,442	38,201	1,491,083	3,951
<b>Maximum Weekday Traffic</b>	43,775	19,399	11,262	1,962	73,277	241
<b>Average Weekday Traffic</b>	37,910	15,406	8,292	1,739	63,347	176
<b>Average Hourly AM Peak Traffic</b>	5,743	1,979	955	212	8,889	N/A
<b>Average Hourly PM Peak Traffic</b>	5,704	2,208	1,145	216	9,273	N/A

Traffic Summary (I-25C)						
	AVI	LPT	HOV	Non-Rev & Hybrid	Total	Hybrid
Total Monthly Traffic	111,734	114,665	55,280	11,356	293,035	1,153
Maximum Weekday Traffic	6,212	6,076	2,444	577	14,965	76
Average Weekday Traffic	5,109	5,092	2,209	516	12,410	53
Average Hourly AM Peak Traffic	747	736	330	72	1,813	N/A
Average Hourly PM Peak Traffic	618	569	272	71	1,459	N/A

Table 1 – Monthly Traffic Summaries

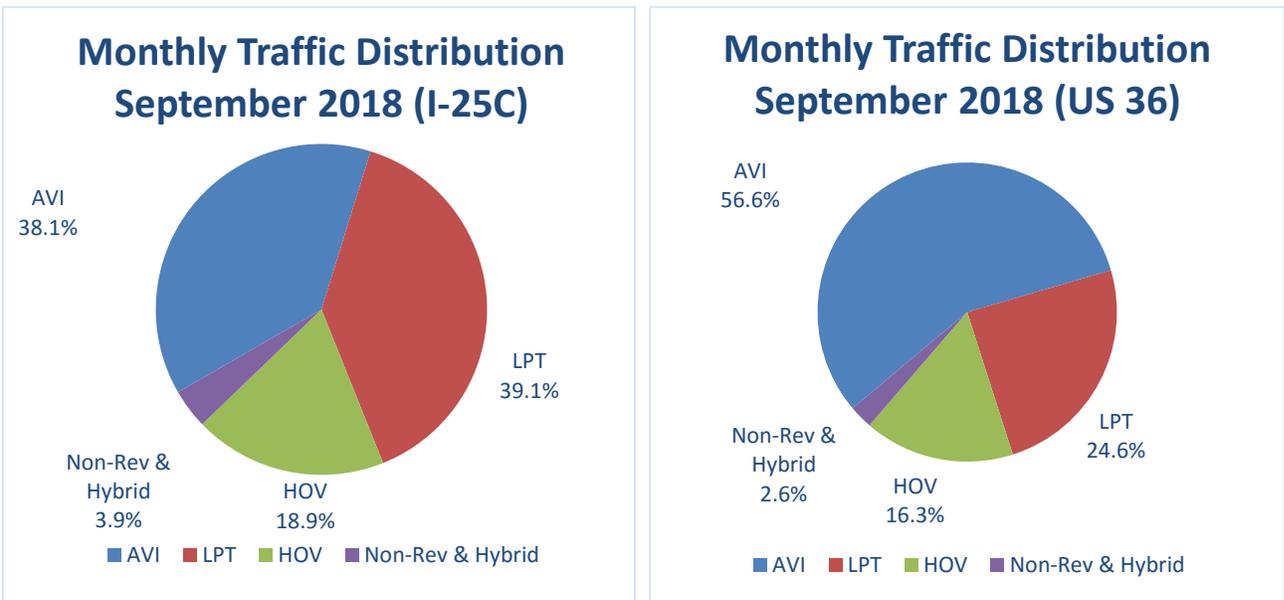
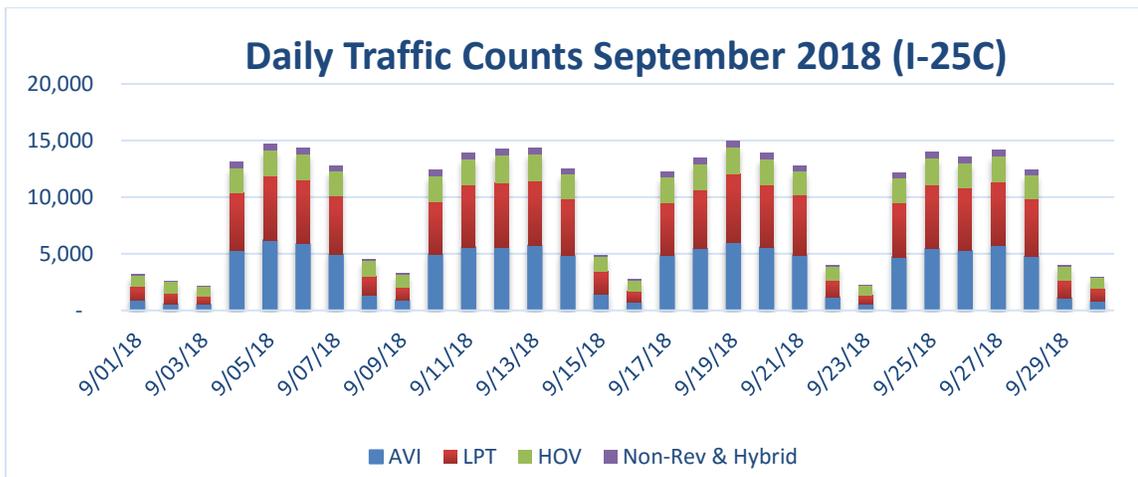


Figure 1 – Monthly Traffic Distribution



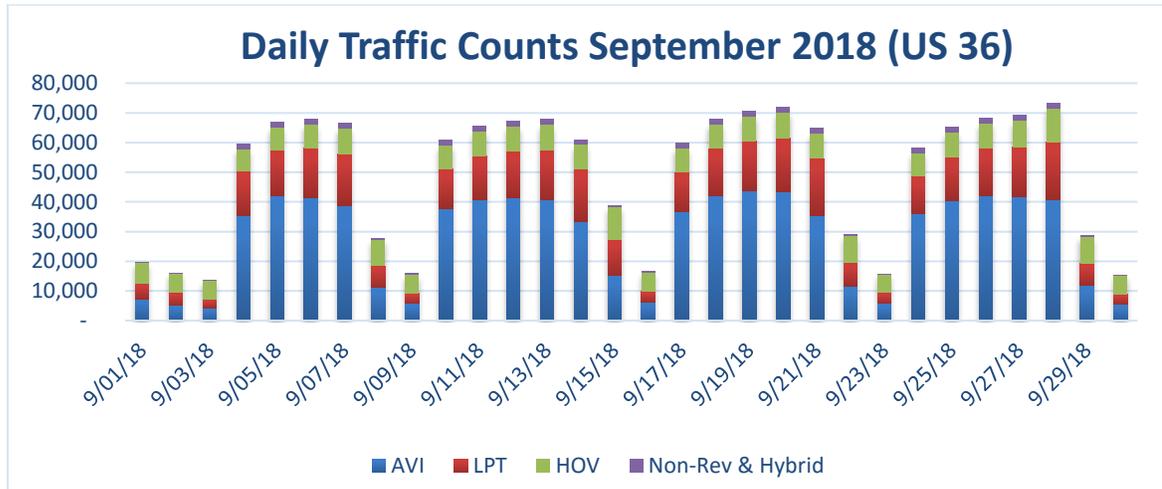


Figure 2 – Daily Traffic Counts

## 2.0 REVENUES

During the month of September 2018, PRD collected \$732,109 and \$809,211 from users of the I-25 Central and US36 Managed Lanes, respectively. For purposes of this report, revenues are recognized at the time of collection, which is typically sometime after they have been incurred for those customers who are billed based on their license plate. For example, if a single-occupant vehicle uses the lanes in October but pays in January, the associated revenue is attributed to January.

## 3.0 OPERATIONAL INCIDENTS, ISSUES, AND CLOSURES

The project had numerous routine debris removals, lighting incidents, guardrail incidents, sign incidents, and graffiti control during the month. The routine lighting, guardrail, roadway markings and sign incidents are all planned for repair within the allowable response period and several previously identified lighting incidents were repaired. All incidents were responded to and rectified within the allowable timeframes.

Date	Start	Stop	Duration
July 3, 2018	15:42	16:20	0:38
July 6, 2018	11:08	12:55	1:47
July 16, 2018	10:09	10:52	0:43
July 20, 2018	15:40	16:32	0:52
July 24, 2018	15:15	16:04	0:49
August 9, 2018	09:25	11:04	1:39
August 10, 2018	16:39	18:11	1:33

August 16, 2018	09:20	10:07	0:47
August 20, 2018	06:45	07:17	0:32
August 21, 2018	17:30	17:56	0:26
August 30, 2018	09:16	10:37	1:21
September 4, 2018	17:15	17:52	0:37
September 9, 2018	02:39	03:10	0:31
September 19, 2018	06:35	07:09	0:34
September 19, 2018	17:23	18:40	1:17
September 20, 2018	10:31	12:18	1:47
September 26, 2018	15:45	16:21	0:36
<b>Total</b>			<b>16 hours 32 minutes</b>
Remaining Closure Hours Available (Ref: CA 29.7)			0 hours 0 minutes

Table 2 – Managed Lanes Closures to Date

The table below provides a listing of ETCS items recorded this month, consistent with Appendix 6-2 of Schedule 6.

Element ID	Cat	Element	Performance Item	PRD Notified	Contractual Cure Period	Cure Achieved
None						

Table 3 – ETCS Issues per CA Schedule 6 Appendix 6-2

The table below provides a status of all Noncompliance categories in accordance with paragraph 1.2 of Schedule 10.

Non-compliance Location	Nature	Cause	Cure Date	Uncured Non-compliance Point	Unexpired Non-compliance Point	365 Day Expiration Date	1095 Day Expiration Date
Promenade West Toll Point	Incorrect toll schedule	Incorrect Toll Schedule was applied during a software update on 3/7/16	3/16/16 (Period II) Customer Accounts Corrected	0	3	3/16/17	3/16/19

Table 4 – Status of Noncompliance Categories

#### 4.0 MEAN TIME BETWEEN FAILURE (MTBF) AND MEAN TIME TO REPAIR (MTTR)

Mean Time Between Failure (MTBF) and Mean Time To Repair (MTTR) data is provided in the table below. Only Maintained Elements that were repaired during the reporting period and had a failure type breakdown are listed in the table. We consider a breakdown to be a failure when the element cannot be used for its intended purpose until repaired.

Maintained Element	Mean Time Between Failure (MTBF) (Hours)	Mean Time To Repair (MTTR) (Hours)
None	N/A	N/A

Table 5 – Mean Time Between Failure & Mean Time To Repair

#### 5.0 HYBRID UTILIZATION

Total Hybrid Trips	
I-25 Central	1,153
US 36	3,951

Table 6 – Hybrid Utilization

Fuel-efficient “Hybrid” vehicles are permitted to access the Express Lanes free of charge, regardless of occupant numbers, provided that they have obtained a permit from CDOT, obtained a Hybrid transponder from E-470, and display an E-470 Hybrid decal on the vehicle’s windshield.

OPERATIONS AND  
MAINTENANCE  
MONTHLY REPORT  
SEPTEMBER 2018

US 36 and I-25 Express  
Lanes Project

Prepared for:

Plenary Roads Denver, LLC  
1700 Lincoln Street, Suite 3000  
Denver, CO 80203

Attention: Mr. Christian Guevara, PE




Prepared By:

Ferrovial Services  
10525 West 120<sup>th</sup> Avenue  
Broomfield, CO 80021  
United States of America

Justin Doles, PE  
Project Manager


OPERATIONS AND MAINTENANCE – MONTHLY REPORT  
 SEPTEMBER 2018  
 US 36 and I-25 Express Lanes Project

Revision	Date	Approved
Rev. 0	10/08/2018	

This report titled *Operations and Maintenance Monthly Report, September 2018* has been prepared by Ferrovial Services for the exclusive use of Plenary Roads Denver, LLC (PRD). No other party is an intended beneficiary of this report or the information, opinions, and conclusions contained herein. Any use by any party other than PRD of any of the information, opinions, or conclusions is the sole responsibility of said party. The use of this report shall be at the sole risk of the user regardless of any fault or negligence of PRD or Ferrovial Services.

The information and analyses contained herein have been completed to a level of detail commensurate with the objectives of the assignment and in light of the information made available to Ferrovial Services at the time of preparation. This report and its supporting documentation have been reviewed and/or checked for conformance with industry-accepted norms. To the best of the information and belief of Ferrovial Services, the information presented in this report is accurate to within the limitations specified herein.

This report is Ferrovial Services pdf file: OM Monthly Report September 2018.pdf. Any reproductions or modifications of this report are uncontrolled and may not be the most recent revision.



---

The O&M Monthly Report contains all relevant information for the month of September 2018. Ferrovial Services continues ongoing and preventive maintenance activities for the I-25 and US36 Managed Lanes Project.

### Ferrovial Services Commitment to Safety

Ferrovial Services conducted weekly toolbox talk meetings during the month. The purpose of the tool box talks is to cover important safety items that relate to the project such as near misses, “better ways” as to how safety is conducted for the Project, and discussion on safety procedures for maintenance activities. In addition to the toolbox talks, Ferrovial Services conducts a weekly progress meeting. This is a forum for feedback from staff on Operations, Incident Response, and Maintenance activities.

Toolbox Talks this month included:

- Face Shields
- Wheel Lug Nut Indicators
- Prevent Head Injuries
- Trailer Hitch Safety
- Winter Gear

### A. Summary of the Planned Maintenance Activities for the Upcoming Month – October 2018

Ferrovial Services has identified the upcoming planned maintenance activities as described in Table 1.7.1.3 of The Maintenance Management Plan. These activities include preventative and routine maintenance in order to successfully operate and maintain the Project. A listing of the planned maintenance activities for the month of October 2018 is included below.

**FIG. A-1 Planned Maintenance Activities for October 2018**

X – INDICATES THE DAY THE TASK IS PLANNED.

Work Activity-Description	Frequency	Oct-18																														
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
		M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W
MAINTENANCE PATROL	Daily	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X
FLEXIBLE PAVEMENT OBSERVATION / REPAIR	F-52	X							X							X								X							X	
RIGID PAVEMENT OBSERVATION / REPAIR	F-52	X							X							X								X							X	
CRACK SEALING	F-1								X	X																						
CONCRETE JOINT SEALING	F-1		X	X	X				X	X	X	X				X	X	X	X													
PAVEMENT STRIPING	F-1	X	X																													
DELINEATORS & MARKERS OBSERVE / CLEAN / REPAIR	F-12			X														X														
DRAINAGE STRUCTURE (INLET) INSPECTION	F-1		X														X															
DRAINAGE (INLET) OBSERVE/ CLEAN / REPAIR	F-12		X						X								X							X							X	
GUARDRAIL, SAFETY BARRIER	F-12				X														X													
IMPACT ATTENUATORS	F-12				X														X													
SIGN OBSERVATION / REPAIR	F-52	X							X								X							X							X	
ELECTRICAL SUPPLY INSPECTION / REPAIR	F-12					X																										
ACCESS PANEL OBSERVATION / REPAIR	F-12					X																										
HERBICIDE & WEED CONTROL MAINTENANCE	F-52			X							X							X							X							X
GRAFFITI OBSERVATION / REMOVAL	F-52	X							X								X							X							X	
LITTER OBSERVATION / REMOVAL	Daily	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X
NODE BUILDING 2 MAINTENANCE	F-1					X															X											
SAND STORAGE DOME MAINTENANCE	F-1											X															X					
LIQUID STORAGE FACILITY MAINTENANCE	F-1											X															X					
REVERSIBLE LANE OPERATIONS	Daily	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X
GATE MAINTENANCE & REPAIR		X							X							X							X							X		

Frequency of Activity:

Daily – Daily Activity


F-4 – Quarterly Activity

F-52 – Weekly Activity

F-2 – Semi-Annual Activity

F-12 – Monthly Activity

F-1 – Annual Activity




## B. Summary of Performed and Completed Maintenance Activities

Fig. B-1 Performed and Complete Maintenance Activities for September 2018

X Indicates the day of the month that the task was completed.

Performance Standard Identification Number (Table 6.1)	Work Activity-Description	Frequency	Sep-18																														
			1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
			S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	
ML-1	MAINTENANCE PATROL	Daily				X	X	X	X										X	X	X	X	X				X	X	X	X	X		
ML-1	FLEXIBLE PAVEMENT OBSERVATION / REPAIR	F-52					X					X									X								X				
ML-1	RIGID PAVEMENT OBSERVATION / REPAIR	F-52					X					X									X								X				
ML-9	CONCRETE JOINT SEALING	F-1																	X	X	X	X				X	X	X	X				
ML-4	DELINEATORS & MARKERS OBSERVE / CLEAN / REPAIR	F-12											X																				
ML-2	DRAINAGE (INLET) OBSERVE/ CLEAN / REPAIR	F-12						X																									
ML-2	DRAINAGE (PIPE/CULVERT) OBSERVE / CLEAN / RPR	F-12						X																									
ML-5.1	GUARDRAIL, SAFETY BARRIER																			X	X												
ML-6	SIGN OBSERVATION / REPAIR	F-52				X					X								X							X							
ML-8	STREET LIGHTING OBSERVATION /REPAIR	F-52				X					X								X							X							
ML-8	ELECTRICAL SUPPLY INSPECTION / REPAIR	F-12																									X						
ML-8	ACCESS PANEL OBSERVATION / REPAIR	F-12																								X							
ML-10	HERBICIDE & WEED CONTROL MAINTENANCE	F-52					X					X									X							X					
ML-12	GRAFFITI OBSERVATION / REMOVAL	F-52					X					X									X												
ML-14	MECHANICAL ROAD SWEEPING	F-12																	X	X	X	X											
ML-14	LITTER OBSERVATION / REMOVAL	Daily				X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	X		
ML-15	NODE BUILDING 2 MAINTENANCE	F-1												X																			
ML-15	SAND STORAGE DOME MAINTENANCE	F-1											X																				
ML-15	LIQUID STORAGE FACILITY MAINTENANCE	F-1										X																					
	REVERSIBLE LANE OPERATIONS	Daily				X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	X		



*Fig. B-2 Work Accomplished This Month*

<b>Activity</b>	<b>Actual Work</b>
152 Asphalt Pavement Surface Rpr (YD2)	4
153 Concrete Pavemnt Surface Rpr (YD2)	5
157 Hnd Crck Seal Rigid Pave (LF)	4,607
162 Surface Shoulder Rprs (MI)	3
202 Clean Drains (EA)	19
210 Slope Repairs (YD3)	135.5
218 Debris in Roadway (HR)	4.5
218 Litter Barrel Trash Cleanup (YD3)	51
220 Sweeping (Mech) (MI)	120
222 Sweeping - Hand (HR)	27
254 Veg Cntrl Hnd/Chem (HR)	20
301 Misc Sign Maint (EA)	12
306 Metal Guardrail Maint (LF)	10
314 Reversible Lane Ops (HR)	291
329 Courtesy Assistance (HR)	313.5
364 Bridge Joint Mnt Cln/Rpr (LF)	3
601 Incident Manag (HR)	4

### C. Summary of Planned Maintenance that was Not Completed for the Month

Ferrovial Services completed all scheduled maintenance activities for the period of September, 2018. Frequencies and/or actual date of the month of some activities may have been adjusted based on actual conditions.

### D. Summary of the Maintenance Activities and Results Performed for the Month Beyond Planned Maintenance

A summary of unplanned maintenance activities provided below:

Snow and Ice Control: None

Courtesy Patrol: None

Hazardous Materials Incidents: None

## E. Operating Contractor's Incident Response Logs Related to Maintenance Activities

This section provides a summary of Ferrovial Services performance related to the Performance and Measurement Criteria listed in Appendix 6-1.1 of the Operating Contract.

The table below provides a listing of items recorded this month:

Element Category	Description	Location	BRS Notified	Response to Defects		
				Category 1		Category 2
				Hazard Mitigation	Permanent Remedy	Permanent Repair
GP5.1	Guardrail (Impact Damage)	I-25 MP 217.22 NB	4/16/2018 15:29:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
GP 8.2	Sign Lighting (L2 Light Out)	US36 MP 56.90 EB	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (South Bulb Out)	040-U36-LHT-0230, MP 56.73	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (South Bulb Out)	040-I25-LHT-0070, MP 214.85	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (All Bulbs Out)	040-I25-LHT-0050, MP 214.73	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
GP 8.2	Sign Lighting (L1 Light Out)	US36 MP 56.60	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
GP 8.2	Sign Lighting (L3 Light Out)	US36 MP 56.60	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
GP 8.2	Sign Lighting (L2 Light Out)	US36 MP 56.60	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (South Bulb Out)	040-U36-LHT-0190, MP 56.47	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (East Bulb Out)	040-U36-LHT-0150, MP 56.22	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (North Bulb Out)	040-I25-LHT-0100, MP 215.02	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (All Bulbs Out)	040-I25-LHT-0020, MP 214.56	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
ML 8.1	Lighting (West Bulb Out)	040-U36-LHT-0220, MP 56.66	5/2/2018 22:00:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
GP6.1	Traffic Sign (Impact Damage)	US36 MP 49.35 WB	5/4/2018 07:30:00	N/A	N/A	Reqd: 6 Months Respnd: 9/10/2018 14:00 Actual: 4.30 Months
GP9.1	Fence (Impact Damage)	US36 MP 42.20 EB	5/14/2018 08:51:00	N/A	N/A	Reqd: 6 Months Respnd: 9/7/2018 13:04 Actual: 3.87 Months
GP6.1	Traffic Sign (Impact Damage)	US36 MP 57.10 EB	5/15/2018 03:30:00	N/A	N/A	Reqd: 6 Months Respnd: 9/10/2018 10:05 Actual: 3.94 Months
GP6.1	Traffic Sign (Impact Damage)	US36 MP 46.80 EB	5/16/2018 15:00:00	N/A	N/A	Reqd: 6 Months Respnd: 9/10/2018 13:05 Actual: 3.89 Months
GP11.2	Erosion (Hail Storm Damage)	US36 MP 40-43.4	5/19/2018 19:16:00	N/A	N/A	Reqd: 6 Months Respnd: -- Actual: In Progress
GP6.1	Traffic Sign (Impact Damage)	US36 MP 53.0 WB	6/26/2018 15:10:00	N/A	N/A	Reqd: 6 Months Respnd: 9/4/2018 13:00 Actual: 2.33 Months

Element Category	Description	Location	BRS Notified	Response to Defects		
				Category 1		Category 2
				Hazard Mitigation	Permanent Remedy	Permanent Repair
ML6.1	Sign (Impact Damage)	US36 MP 53.25 WB	7/6/2018 11:15:00	N/A	N/A	Reqd: 6 Months Resp: 9/4/2018 13:00 Actual: 2.00 Months
ML5.1	Median Barrier (Impact Damage)	US36 MP 53.25	7/6/2018 11:15:00	N/A	N/A	Reqd: 6 Months Resp: -- Actual: In Progress
GP5.1	Guardrail (Impact Damage)	US36 MP 46.7 EB	7/15/2018 10:00:00	N/A	N/A	Reqd: 6 Months Resp: -- Actual: In Progress
GP5.1	Guardrail (Impact Damage)	US36 MP 43.10 EB	8/3/2018 15:50:00	N/A	N/A	Reqd: 6 Months Resp: -- Actual: In Progress
GP5.1	Guardrail (Impact Damage)	US36 MP 40.2 WB	8/23/2018 07:56:00	N/A	N/A	Reqd: 6 Months Resp: -- Actual: In Progress
GP1.1	Debris (Cleared Door from Lanes)	US36 MP 47.00 WB	9/5/2018 10:03:00	Reqd: 1 Hours Resp: 9/5/2018 10:30 Actual: 0.45 Hours	N/A	N/A
GP1.1	Debris (Debris Reported, Nothing Found)	US36 MP 44.00 WB	9/5/2018 06:30:00	Reqd: 1 Hours Resp: 9/5/2018 06:55 Actual: 0.41 Hours	N/A	N/A
GP1.1	Debris (Cleared Wood from Lanes)	US36 MP 54.8 WB	9/6/2018 14:55:00	Reqd: 1 Hours Resp: 9/6/2018 15:43 Actual: 0.79 Hours	N/A	N/A
GP1.1	Debris (Cleared Tire from Lanes)	US36 MP 55.3 WB	9/11/2018 16:20:00	Reqd: 1 Hours Resp: 9/11/2018 16:48 Actual: 0.46 Hours	N/A	N/A
GP1.1	Debris (Cleared Tire from Lanes)	US36 MP 54.8 WB	9/11/2018 16:05:00	Reqd: 1 Hours Resp: 9/11/2018 16:46 Actual: 0.68 Hours	N/A	N/A
GP1.1	Debris (Cleared Sign from Lanes)	US36 MP 54.6 EB	9/11/2018 15:36:00	Reqd: 1 Hours Resp: 9/11/2018 16:10 Actual: 0.56 Hours	N/A	N/A
GP5.1	Guardrail (Impact Damage)	US36 MP 54.80 WB	9/12/2018 14:18:00	N/A	N/A	Reqd: 6 Months Resp: -- Actual: In Progress
GP5.1	Guardrail (Impact Damage)	US36 MP 54.4 WB	9/12/2018 08:00:00	N/A	N/A	Reqd: 6 Months Resp: -- Actual: In Progress
GP1.1	Debris (Cleared Tarp from Lanes)	US36 MP 54.8 EB	9/17/2018 16:03:00	Reqd: 1 Hours Resp: 9/17/2018 17:00 Actual: 0.95 Hours	N/A	N/A
GP1.1	Debris (Cleared Metal from Lanes)	US36 MP 55.9 WB	9/19/2018 11:34:00	Reqd: 1 Hours Resp: 9/19/2018 12:31 Actual: 0.94 Hours	N/A	N/A
GP1.1	Debris (Cleared Ladder from Lanes)	US36 MP 45.8 EB	9/19/2018 12:48:00	Reqd: 1 Hours Resp: 9/19/2018 13:33 Actual: 0.75 Hours	N/A	N/A
ML13.1	Incident Response (Responded to Accident per CSP Request)	US36 MP 42.40	9/20/2018 10:23:00	Reqd: 1 Hours Resp: 9/20/2018 10:33 Actual: 0.16 Hours	N/A	N/A
GP1.1	Debris (Debris Reported, Nothing Found)	US36 MP 56.00 EB	9/20/2018 16:08:00	Reqd: 1 Hours Resp: 9/20/2018 17:00 Actual: 0.86 Hours	N/A	N/A
GP1.1	Debris (Debris Reported, Nothing Found)	US36 MP 45.8 WB	9/21/2018 05:42:00	Reqd: 1 Hours Resp: 9/21/2018 06:19 Actual: 0.61 Hours	N/A	N/A
GP1.1	Debris (Cleared Ladder from Lanes)	US36 MP 54.30 WB	9/25/2018 17:59:00	Reqd: 1 Hours Resp: 9/25/2018 18:27 Actual: 0.46 Hours	N/A	N/A

Element Category	Description	Location	BRS Notified	Response to Defects		
				Category 1		Category 2
				Hazard Mitigation	Permanent Remedy	Permanent Repair
GP1.1	Debris (Cleared Chair from Lanes)	US36 MP 46.60 EB	9/25/2018 18:26:00	Reqd: 1 Hours Resp'd: 9/25/2018 19:03 Actual: 0.61 Hours	N/A	N/A
GP1.1	Debris (Cleared Glass from Lanes)	US36 MP 37.80 EB	9/27/2018 09:39:00	Reqd: 1 Hours Resp'd: 9/27/2018 09:55 Actual: 0.26 Hours	N/A	N/A
GP1.1	Debris (Cleared Debris from Lanes)	US36 MP 52.9 EB	9/28/2018 09:23:00	Reqd: 1 Hours Resp'd: 9/28/2018 09:45 Actual: 0.36 Hours	N/A	N/A

All items were completed within the required response time. Items that are *In Progress* are still within the allowed response time.

## F. Detailed Results of All Inspections, Assessments, and Testing Activities

During this reporting period there were no special inspections, assessments, or testing results outside normal operating condition.

## G. Monthly Toll System Performance Reports

Toll system operated within proposed parameters per Ferrovial Services observations.

## H. Preventative Maintenance Plan and Progress

Preventative Maintenance work is contingent on Initial Works Package implementation.

## I, J. Mean Time between Failure (MTBF), Mean Time To Repair (MTTR)

No Maintained Elements experienced a failure type breakdown this month. Ferrovial Services considers a breakdown to be a failure when the element cannot be used for its intended purpose until repaired.
